

GRANT AWARD AGREEMENT

Fiscal Year 2020 Class A Incentive Grant Program

THIS AGREEMENT, made and entered into on the 1st day of May, 2020, by and between the **LEXINGTON-FAYETTE URBAN COUNTY GOVERNMENT**, an urban county government of the Commonwealth of Kentucky, pursuant to KRS Chapter 67A (hereinafter "Government"), on behalf of its Division of Water Quality, and **WARRENTON WOODS STREET MAINTENANCE ASSOCIATION, INC.**, 3144 WARRENWOOD WYND, LEXINGTON, KENTUCKY 40502, (hereinafter "Grantee").

WITNESSETH:

WHEREAS, the Government has funds available through the Stormwater Quality Projects Incentive Grant Program to assist qualified applicants in the implementation of projects that meet the goals of the program; and

WHEREAS, the Grantee represents directly or indirectly a group of single-family residences in Fayette County who are fee-payers of the Government's Water Quality Management Fee; and

WHEREAS, the Grantee has proposed a need for the funds requested to develop and implement a proposed project by submitting a valid grant application; and

WHEREAS, the Grantee desires to implement a specific project that meets one or more Incentive Grant program goals to improve water quality, reduce stormwater runoff, and provide public or private education related to stormwater quality for the benefit of its members, community, and the general public; and

WHEREAS, the Grantee's grant application has been reviewed and selected for funding by the Government's Water Quality Fees Board in accordance with Sections 16-408 and 16-410 of the Government's Code of Ordinances;

THAT FOR AND IN CONSIDERATION OF THE MUTUAL PROMISES AND COVENANTS HEREIN EXPRESSED, GOVERNMENT AND GRANTEE AGREE AS FOLLOWS:

- (1) The Government hereby grants the Grantee the sum of **\$49,450.00** (hereinafter "the Grant"), for use in implementing the project elements as listed in Attachment A which is incorporated herein by reference as if fully set out herein.
- (2) The Grantee agrees to match the Grant with contributions, labor and other services equal to or greater than 20% of the total project cost.
- (3) The Grantee agrees to use the Grant only for the activities set forth in Attachment A.
- (4) The Grantee agrees to perform periodic reporting as detailed in Paragraph 5 herein below,

(5) The Grant to the Grantee shall be disbursed in the following manner:

- (a) The Grantee shall submit, at least once every three (3) months, a *Grant Reimbursement Form* and a *Request for Funds*, in standardized format provided by the Government, to the Government's Grant Manager designated by the Director of the Division of Water Quality for the project. The *Request for Funds* shall include documentation that the Grantee has already expended the requested funds or shall be in a position to expend properly the requested funds within thirty (30) days of receipt of the funds. The *Request for Funds* shall include full accounting of all eligible grant-related expenses, as listed in Attachment A. Copies of invoices, purchase orders, or receipts showing vendor, date, amount, and items purchased or ordered shall be provided with the *Request for Funds*.
 - (b) Each *Request for Funds* shall include documentation of all of the Grantee's Match Costs listed in Attachment A and claimed for the prior period. For cash expenditures this shall include receipts, showing vendor paid, date, amount, and items purchased. For volunteer hours this shall include sign-in sheets describing the events with signatures, name, address, time in and time out (or length of event), for each participant (volunteers must be 12 years of age or older). For mileage, this shall include driver name, type of vehicle, location to and from, date, and miles driven.
 - (c) Each *Request for Funds* shall be accompanied by a *Project Status Report*, in a standardized format provided by the Government, describing the progress of the project to date, including a description and schedule of all activities completed, and hardcopy or electronic copies of materials completed and/or used to date. For educational events (if applicable), copies of the class sign-in sheets documenting the number of attendees shall be provided.
 - (d) The Government's Grant Manager shall review each *Request for Funds* and supporting documents for compliance with the terms of this Agreement and the guidelines of the Stormwater Quality Projects Incentive Grant Program. If the Government's Grant Manager finds the Grantee's *Request for Funds* is in compliance with the terms of this Agreement and the Program's guidelines and that the activity progress and management program of the Grantee satisfy the terms of this Agreement, he or she shall approve the *Request for Funds* within 15 days of receipt, and then forward it to the Division of Accounting for payment.
 - (e) Should the Government's Program Administrator determine that the Grantee is not in compliance with the terms of this Agreement and/or the Stormwater Quality Projects Incentive Grant Program, including deficiencies in progress and/or management of the project, the Division of Water Quality shall notify the Mayor's Office and the appropriate district Council person and shall meet with the Grantee on matters that prevent approval of the *Request for Funds*. Failure to resolve any such matters to the satisfaction of the Government may lead to termination of the Agreement for cause pursuant to Paragraph 25 herein below.
 - (f) The Government shall release payment of the final 3% of the Grant only after receipt and acceptance of the Project Final Report. The Government's Grant Manager shall review the Project Final Report and provide comments to the Grantee within 15 calendar days or, if acceptable, forward approval to the Division of Accounting for payment.
- (6) For any project which includes installation of permanent capital infrastructure as listed in Attachment A (not to include individual rain barrels, small rain gardens, and nond equip-

- (7) For any project which includes installation of permanent capital infrastructure as listed in Attachment A, the Grantee agrees to provide in hard copy and electronic format the following deliverables as they become available, each sealed by a Professional Engineer licensed in the Commonwealth of Kentucky (or Registered Landscape Architect when allowed by Kentucky Revised Statutes 323A.010):
- Design calculations;
 - Final construction plans, including erosion and sediment control plans, traffic control plans, grading plans, etc.;
 - Final specifications and bidding documents (if applicable);
 - Detailed engineer's construction cost estimate including quantities;
 - Inspection, Operation, and Maintenance Plan laying out the plan for regular inspection and maintenance of each proposed facility for design performance and safety in accordance with manufacturer's specifications and the Government's Stormwater Manual.
 - Copies of all federal, state, and local permits, approvals, encroachments, etc. obtained for the project.
 - Record Drawing showing all field changes, and signed and sealed by the professional of record certifying the project as shown meets all original design intent.
 - Photo documentation of site conditions and improvements before, during, and after construction.
- (8) For any project which includes installation of permanent capital infrastructure listed in Attachment A, the Grantee shall provide, by the end of the design phase, certification by a Professional Engineer or Registered Landscape Architect licensed in Kentucky that all stormwater control facilities proposed for this project are feasible and viable Best Management Practices (BMPs) for controlling stormwater quality and/or quantity and are appropriate for the project site.
- (9) The Grantee agrees that any and all stormwater control facilities, including equipment and infrastructure, constructed or purchased with Grant monies shall remain the property of the Grantee, or the current property owner, or his successors and assigns, unless otherwise noted in Attachment A.
- (10) The Grantee agrees that all stormwater control facilities, including equipment and infrastructure shall remain in service and maintained by the Grantee or its representatives for at least the Service Life listed in Attachment A. For capital infrastructure, this shall include following the Inspection, Operation, and Maintenance Plan developed for each facility referenced in Paragraph 7 above. For capital infrastructure, the Grantee further accepts and agrees to enter into the "*Agreement to Maintain Stormwater Control Facilities for Class A Incentive Grant Projects*" attached hereto as Attachment B and which is incorporated herein by reference as if fully set out herein.
- (11) The Grantee agrees, and all individual property owners with grant-funded improvements installed on their properties shall agree, to allow the Government access to perform monitoring of the project elements for compliance with this Agreement.
- (12) The Grantee agrees to comply with all applicable local, state, and federal rules, regulations, ordinances, and laws in implementation of the project.
- (13) The Grantee agrees to obtain all necessary local, state, and federal permits and approvals in a timely manner and prior to the start of any work requiring such permits or approvals.
- (14) The Grantee agrees to obtain written approval from the Government's Grant Manager or Program Administrator for any proposed changes to the Project Team or Project Plan as

from the date of this Agreement. The Grantee agrees to obtain written approval from the Government's Grant Manager or Program Administrator for any time extensions beyond the grant period. Failure to gain written approval prior to making changes may lead to termination of the Agreement for cause pursuant to Paragraph 25 herein below.

- (16) The Grantee understands that the Grant shown herein in Paragraph 1 is a not-to-exceed amount, and any additional funding needed to complete the project elements listed in Attachment A is the responsibility of the Grantee. If it becomes apparent to the Grantee or the Government that the Grantee will be unable to complete the project either in the manner or for the amount described in this Agreement, then the Grantee must immediately notify the Government's Grant Manager and Program Administrator by providing a complete and detailed written explanation of its inability to comply with the terms of the Agreement. The Grantee must further provide the Government's Grant Manager and Program Administrator with a complete and detailed written explanation of any proposed changes, and the reasons for those changes.
- (17) The Grantee asserts that it is an incorporated organization registered in active status with the Commonwealth of Kentucky Secretary of State, and is in full compliance with all applicable provisions of the Lexington-Fayette Urban County Government's Code of Ordinances Chapter 5 – Buildings and Building Regulations, Chapter 7 – Finance and Taxation, Chapter 12 – Housing, and Chapter 16 – Sewage, Garbage, Refuse, and Weeds, or in compliance with Kentucky Department of Housings Buildings and Construction rules and requirements as is appropriate for those state institutions, parcels, or buildings which are subject to state regulations and oversight as opposed to local ordinances and regulations. If the Grantee becomes out of compliance with any of these provisions, it will contact the Government's Program Administrator immediately. Failure to resolve any such matters to the satisfaction of the Government may lead to termination of the Agreement for cause pursuant to Paragraph 25 herein below.
- (18) This Agreement may not be modified except by written agreement of the Government and the Grantee.
- (19) In any advertisement of the grant-funded project, whether oral or written communications, the Grantee agrees to identify the Lexington-Fayette Urban County Government as the source of the above referenced funds; the Grantee shall not specifically identify any individual or elected official as being responsible for the funds donated by the Government.
- (20) The Grantee agrees to allow the Government to publicize the Grantee's project through the Government's website and other media.
- (21) The Grantee agrees to reference the Lexington-Fayette Urban County Government's Water Quality Management Fee and the Stormwater Quality Projects Incentive Grant Program as a source of funding for the project on any permanent signage or educational brochures, presentations, websites, etc. produced using grant monies.
- (22) The Grantee is solely responsible for assuring that adequate and appropriate insurance or other necessary coverage is maintained during the term of this Agreement.
- (23) The Grantee shall provide equal opportunity in employment as required by applicable federal, state, and local laws, regulations and ordinances.
- (24) The Government assumes no responsibility whatsoever in the Grantee's project activities. Grantee shall defend, indemnify, and hold harmless the Government from and against any and all liability, claims, damages, losses, actions, costs, expenses, obligations, fines, and assessments of whatever kind, including defense costs and attorney's fees that are in any way

ments or stipulations of this Agreement, the Government shall provide the Grantee thirty (30) calendar days to address the deficiency or violation. If the Grantee does not, after the thirty (30) days, come into compliance with this Agreement, the Government shall thereupon have the right to terminate this Agreement by giving written notice to the Grantee of such termination and specifying the effective date thereof, at least five (5) calendar days before the effective date of such termination. In that event, all finished or unfinished documents, receipts and reports prepared by the Grantee shall, at the option of the Government, become its property and the Grantee shall immediately repay to the Government all monies received pursuant to this Agreement less any amount representing just and equitable compensation for the Government's share of any satisfactory work completed pursuant to the Agreement.

- (26) The Grantee's sole remedy for a breach of this Agreement by the Government shall be limited to the amount of the Grant.

IN WITNESS WHEREOF, the parties hereto have executed this Agreement at Lexington, Fayette County, Kentucky, this the day and year first above written.

**LEXINGTON-FAYETTE URBAN COUNTY
GOVERNMENT**

BY: *Linda Gorton*

LINDA GORTON, MAYOR

ATTEST:

Mackenzie Sommer
CLERK, URBAN COUNTY COUNCIL

**Grantee Organization: WARRENTON WOODS STREET MAINTENANCE
ASSOCIATION, INC.**

3116 ~~3114~~ WARRENWOOD WYND

LEXINGTON, KY 40502

BY: *Gertrude Tibbs*

NAME: *Gertrude Tibbs*

TITLE: *President*

ATTACHMENT A
to the GRANT AWARD AGREEMENT
between Lexington-Fayette Urban County Government (LFUCG) and
Warrenton Woods Street Maintenance Association, Inc. (WWSMA)

GRANT PROGRAM **FY2020 Stormwater Quality Projects Incentive Grant Program**
Class A (Neighborhood) Projects

- Funded through the LFUCG Water Quality Management Fee
- Administered by the LFUCG Division of Water Quality in the Department of Environmental Quality and Public Works

PROJECT TEAM AND CONTACT INFORMATION

Grantee Organization: Warrenton Woods Street Maintenance Association, Inc. (WWSMA) GT
3144 Warrenwood Wynd
Lexington, KY 40502
KY Organization #0083770

Organization President: Trudy Tibbs
859-229-8485 (phone)
trudytibbs27@gmail.com (email)

Primary Project Contact: Andy Henderson
859-221-6966 (phone)
ahend@lexclin.com (email)

Secondary Project Contact & Project Manager: Sue Ann Hillman
859-280-6435 (phone)
hellosueann@gmail.com (email)

Project Site Location: 3136, 3140, 3144, 3157 Warrenwood Wynd; 1404 & 1405 Meganwood Circle

Property Owners: See Table 3

Design Engineering Firm: Bell Engineering
2480 Fortune Drive
Lexington, KY 40509
859-278-5412 (phone)
Jonathan Rehner, P.E. (Engineer of Record)
jrehner@hkbell.com (email)

Contractor: To Be Determined

PROJECT PLAN ELEMENTS

All improvements shall be located on the private properties listed in this Attachment A, Table 3. No other property or Right-of-Way shall be disturbed without the written permission from the property owners and/or LFUCG.

The objectives of this project are to improve water quality by reducing runoff, and to provide stormwater education to the WWSMA community.

1) ELEMENTS:

- C. Swale Installation – Create a defined swale cross section, including a newly defined rock channel using articulated concrete blocks.
- D. Education – Stormwater education in the form of a presentation consisting of methods used to reduce runoff and improve water quality, and if needed flyers for all non-attendees.

2) **DESIGN:**

No grant-funded activities shall occur until the LFUCG Grant Manager gives notice-to-proceed, in writing, for the start of the design phase of the project.

Design tasks will include meetings, survey, engineering design, permit submittals to the applicable local, state, and federal agencies, bidding, and construction.

Design shall also account for the following stipulations:

- Submittals for stream permits (401/404) shall be completed as early as possible in the design process to inform the Design Engineer of alternatives that can be permitted without triggering state or federal mitigation requirements (if required).
- The Design Engineer shall meet with the LFUCG Grant Manager for at least three meetings during the design phase:
 - i) Prior to the start of design
 - ii) At the completion of approximately 50% design
 - iii) At the 95% completion of the design documents

The Design Engineer shall provide a copy of the preliminary plans (working drawings), calculations, and specifications (if available) representing 50% and 95% completion. These submittals shall be used to assist LFUCG staff in understanding the project components and allow for feedback to ensure the Government's funds shall be utilized for sustainable and effective infrastructure.

- All existing utilities shall be located and shown on the design plans.
- All existing easements, adjacent property lines, and Rights-of-Way shall be shown on the design plans. If any work is proposed to occur within any easement (i.e., utility, etc.), whether public or private, the Organization shall obtain all necessary encroachment agreements from the authorized agencies prior to the start of construction.
- Any work proposed within or on public right-of-way, easement, or LFUCG-owned property will require one or more permits or approvals. This includes installation permits for connection into any existing curb inlet or stormwater manhole located within public right-of-way. Please contact the appropriate staff:

Environmental Services (street trees), Tim Queary – tqueary@lexingtonky.gov
 Engineering (right-of-way), Brian Knapp – bknapp@lexingtonky.gov
 Sanitary Sewers, Rod Chervus – rchervus@lexingtonky.gov
 Stormwater, Greg Lubeck – glubeck@lexingtonky.gov

- All federal, state, and local permits, approvals, and agreements required for construction of the proposed improvements shall be obtained prior to the start of construction. If the timing of construction is such that a permit may expire before construction can be completed, then the Organization shall coordinate with the LFUCG Grant Manager and permitting agencies

3) **CONSTRUCTION:**

Facilities shall be constructed per the design plans and specifications. Construction of the proposed facilities shall also meet the following stipulations:

- **No construction shall occur until written approval from all affected property owners is provided to the LFUCG Grant Manager.**
- Construction shall not begin until all permits, approvals, agreements, etc. are obtained and copies provided to the LFUCG Grant Manager.
- All existing utilities shall be contacted, located, and coordinated with prior to any work being performed.
- The Erosion and Sediment Control Plan shall be provided to LFUCG for review and comment. The LFUCG Land Disturbance Permit shall be obtained by the contractor after placement of the ESC and traffic control measures.
- Failure to place acceptable erosion and sediment control measures into service prior to start of construction will result in shut-down of the job site until the measures are put in place. Construction practices shall be put in place to prevent the illicit discharge of sediment, dirt, sand, fluids, trash, and any other pollutant into the Municipal Separate Storm Sewer System or Waters of the Commonwealth.
- The Organization shall host a pre-construction meeting with all parties. The LFUCG Grant Manager shall be invited to this meeting and given 3 business days notice.
- The Organization is responsible to provide all construction oversight, administration, and daily inspection. LFUCG shall not provide these services.
- The Organization shall document construction by taking before, during, and after photographs.
- Once construction is complete, a final walk-thru inspection shall be performed. The LFUCG Grant Manager shall be invited to this inspection and given 5 business days notice. If punch-list items are identified, a second inspection shall be performed once those items are resolved, and the LFUCG Grant Manager shall be invited to this inspection and given 5 business days notice.
- The Organization agrees to enter into the *Agreement to Maintain Stormwater Control Facilities for Class A Incentive Grant Projects* included as Attachment B of the Grant Award Agreement within 21 calendar days of the final (post punch-list) inspection. This Agreement may be recorded by LFUCG at the Fayette County Clerk's office.

REPORTING REQUIREMENTS

- 1) At the completion of the Design Phase, the Organization shall provide the LFUCG Grant Manager three (3) hard copies and one (1) digital copy each of the following six (6) deliverables, each sealed by a professional licensed to perform such work in accordance with Kentucky Revised Statutes (KRS):

- Set of all final design calculations
- Set of final construction plans, including erosion and sediment control plans, grading plans, etc.
- Set of final specifications and bidding documents (if applicable)

- 2) The Organization shall allow LFUCG twenty-one (21) calendar days to review the submittals and provide comments. If revised submittals are required, the Organization shall allow LFUCG ten (10) calendar days for review per submittal. LFUCG may choose to have a third party engineering consultant assist LFUCG in review of these submittals.
- 3) **The design phase shall end when the LFUCG Grant Manager provides written acceptance of the design submittals.**
- 4) If the project is to be competitively bid, the selected contractor's unit price contract/bid list shall be provided to the LFUCG Grant Manager prior to the start of construction.
- 5) If the project is not competitively bid, the selected contractor's unit price contract shall be provided to the LFUCG Grant Manager prior to the start of construction, along with a justification for any derivations from the engineer's construction cost estimate.
- 6) The Organization shall submit copies of all required local, state, or federal permits, approvals, public or private encroachment agreements, etc. to the LFUCG Grant Manager prior to the start of construction.
- 7) Copies of written approval/agreement from affected property owners shall be provided to the LFUCG Grant Manager prior to proceeding with construction.
- 8) **The construction phase shall begin only after the LFUCG Grant Manager gives notice-to-proceed, in writing, for the start of the construction phase of the project.**
- 9) If, during construction, the contractor requests a deviation or addition to the quantities or costs in the construction contract, the LFUCG Grant Manager shall be notified within 2 business days. Additions or modifications to the project that are not directly related to the intended and correct function of the stormwater control project elements as described in the Project Plan Elements listed above and in original incentive grant application are not eligible for Grant reimbursement. Therefore, the Organization is advised that it should coordinate closely with the LFUCG Grant Manager during construction to ensure the work being performed is in compliance with this Agreement. Note that per the Grant Award Agreement all over-runs that result in the project costs exceeding the Grant amount are the responsibility of the Organization.
- 10) After construction is completed, the Project Final Report shall include copies of the following:
 - Summary of final construction costs and quantities
 - Copies of all federal, state, and local permits obtained for the project (if not previously provided)
 - 3 copies of a Record Drawing showing all field changes, and signed and sealed by the professional of record certifying the project as shown meets all original design intent
 - Copies of final inspection minutes, punchlists, etc.
 - Photo documentation of site conditions and improvements before, during, and after construction
 - Signed *Agreement to Maintain Stormwater Facilities Funded by an LFUCG Stormwater Quality Projects Class A Incentive Grant* (Note: This form will be completed after construction is completed and final costs determined.)
- 11) LFUCG shall make final payment of the 3% retainer after acceptance of the Project Final Report.

EDUCATIONAL OPPORTUNITIES

Stormwater education in the form of a presentation consisting of methods used to reduce runoff

Ownership: The proposed permanent facilities are expected to reside on private property in Fayette County and be owned by the property owners.

Future Inspection and Maintenance: The Organization (and/or Property Owner) agrees to sign and abide by the terms of the *Maintenance Agreement for Stormwater Control Facilities for Class A Incentive Grant Projects* included as Attachment B to the Grant Award Agreement. At the end of construction, the Organization may choose to: a) enter into the Agreement with LFUCG and assume responsibility for maintenance or b) enter into the Agreement with LFUCG for responsibility to ensure maintenance, and enter into a second private agreement with the property owners to perform the future maintenance.

Monitoring by LFUCG: The Organization agrees to allow LFUCG staff future access to any property on which work is performed to monitor the installed features for compliance with this Agreement following the grant period. After the grant period has ended, the Organization agrees to allow LFUCG access for monitoring per the terms of the Maintenance Agreement. Water quality sampling via grab samples or other methods may be employed by LFUCG staff as part of LFUCG’s annual reporting requirement of its Kentucky Pollutant Discharge Elimination System (KPDES) MS4 Phase 1 Permit.

GRANT PERIOD & PROJECT SCHEDULE

The grant period starts on the date of execution by the Mayor and extends for the time period as listed in the Grant Award Agreement. Any time extensions must be approved in writing by the LFUCG Grant Manager. The project schedule shown in Table 1 is preliminary. Proposed changes to the project which alter this schedule significantly shall be discussed with the LFUCG Grant Manager prior to implementation.

TABLE 1 – PRELIMINARY PROJECT SCHEDULE

Activity	Schedule
Approval of Grant Award Agreement and Notice to Proceed (NTP)	Anticipated January 2020
Collect field data for design	Within 1 Month of NTP, end of February 2020
Finalize design plans and specifications of the stormwater improvements (articulating concrete blocks, rock channel cross section, raingarden, etc.)	Mid-April 2020
Bid project with qualified contractors. Select a contractor.	Mid-May 2020
Complete Construction	End of July 2020
Advertise Educational Seminar	At the completion of Construction, July 2020
Hold Educational Seminar	Within 1 month of completion of construction
Provide Project Final Report to LFUCG	Within 2 months of completion of construction

ADDITIONAL GRANT STIPULATIONS

1. Organization shall obtain written approval/agreement prior to work being done on private properties and on all properties not owned by the Organization.
2. The project shall not proceed with field work until written approval to proceed is obtained from the Grant Administrator or Director of Water Quality, because of the potential for conflict with future LFUCG Projects.
3. Organization proposes a larger cost share beyond that required by the grant program. Budget shall reflect the 20.2% cost share offered in the application (approximately \$12,550.00).
4. Since the proposed project is slated for multiple properties with different property owners, Organization shall provide the Division of Water Quality with an agreement, in writing, relating to the potential future transfers of ownership relative to future maintenance responsibilities for all project elements involving construction at these proposed locations.

Any work performed on this project prior to grant award by Urban County Council and Notice to Proceed from the LFUCG Grant Administrator is NOT an eligible expense and shall not be reimbursed or counted toward the cost share.

The construction estimate will be revised as part of the design process. The Grant is a not-to-exceed amount, and any cost overruns are the responsibility of the Grantee.

TABLE 2 – PROJECT BUDGET

	Type of Expense	Participants	Item	Unit Price	Quantity	Funded by Organization	Funded by Grant	Total Expense	
1 Project Element: Design and Construction Administration									
2	Professional Design	Bell Engineering	Planning, Design, Construction, Administration.	\$ 6,000.00	LS	1	\$ 6,000.00	\$ - \$ 6,000.00	
3	Professional Design	Bell Engineering	Planning, Design, Construction, Administration	\$ 3,000.00	LS	1	\$ -	\$ 3,000.00 \$ 3,000.00	
4 Project Element: Construction									
5	Materials	Contractor	Straight 12" headwall installed at the top of the swale	\$ 3,000.00	EA	1	\$ -	\$ 3,000.00 \$ 3,000.00	
6	Materials	Contractor	Articulating concrete blocks at beginning of rock channel (6' wide x 10' long)	\$ 50.00	SF	60	\$ -	\$ 3,000.00 \$ 3,000.00	
7	Materials	Contractor	Regrading Existing Swale for proposed natural trapezoidal dry creek channel, 2' - 3' channel bottom by 1' - 1.5' deep with 2:1 sloped sides	\$ 15.00	LF	400	\$ -	\$ 6,000.00 \$ 6,000.00	
8	Materials	Contractor	Rock Stabilized dry creek Channel, minimum 2' Wx1.5' Deep, including filter fabric beneath channel	\$ 35.00	LF	450	\$ -	\$ 15,750.00 \$ 15,750.00	
9	Materials	Contractor	Vegetation Buffer zone along rock stabilized dry creek channel (3' wide on each side), including plants and mulch	\$ 45.00	LF	133	\$ 6,000.00	\$ - \$ 6,000.00	
10	Materials	Contractor	Vegetation Buffer zone along rock stabilized dry creek channel (3' wide on each side), including plants and mulch	\$ 45.00	LF	267	\$ -	\$ 12,000.00 \$ 12,000.00	
11	Materials	Contractor	Raingarden at 3140 Warrenwood Wynd yard inlet per LFUCG Stormwater Manual Figure 10-1 - Bioretention System, 4' wide by 4' deep (8" pea gravel layer with 4" dia perforated PVC pipe, 12" sand bed, 24" planting soil), including plantings	\$ 100.00	LF	25	\$ -	\$ 2,500.00 \$ 2,500.00	
12	Labor	Contractor	Tie the end of proposed swale into the existing concrete channel	\$ 3,000.00	LS	1	\$ -	\$ 3,000.00 \$ 3,000.00	
13	Materials	Contractor	Sodding all disturbed areas	\$ 4.00	SY	300	\$ -	\$ 1,200.00 \$ 1,200.00	
14 Project Element: Educational Seminar									
15	Presentation	Bell Engineering	Education presentation/seminar	\$ 500.00	LS	1	\$ 500.00	\$ - \$ 500.00	
16	Supplies	HOA	Advertising for event: flyers - black & white	\$ 0.50	per flyer	100	\$ 50.00	\$ - \$ 50.00	
TOTAL PROJECT BUDGET:							\$ 12,550.00	\$ 49,450.00	\$ 62,000.00
<div style="border: 1px solid black; padding: 5px; display: inline-block;"> COST SHARE % = 20.24% UK MUST BE > 20% </div>						ORGANIZATION SHARE 20.2%	GRANT SHARE 79.8%		
* Note: Organization share must be 20% of total project costs.									

TABLE 3 – WWSMA - LIST OF AFFECTED PROPERTY OWNERS (AT TIME OF APPLICATION)

Warrenton Woods Street Maintenance Association, Inc. (Water Quality Grant)					
	First Name(s)	Last Name	House #	Street	Preliminary Approval/Agreement
1	Leaon J	Ravlin	1404	Meganwood Circle	Signed
2	Robert E. and Sueannah Wylie	Fox	1405	Meganwood Circle	Signed
3	Andrew H	Henderson	3136	Warrenwood Wynd	Signed
4	Sue Ann	Hilman	3140	Warrenwood Wynd	Signed
5	Robert E.	MacLIN III, (Trustee)	3144	Warrenwood Wynd	Signed
6	Brian	Johnson	3157	Warrenwood Wynd	Signed

FIGURE 1 – WWSMA - MAP OF AFFECTED PARCELS


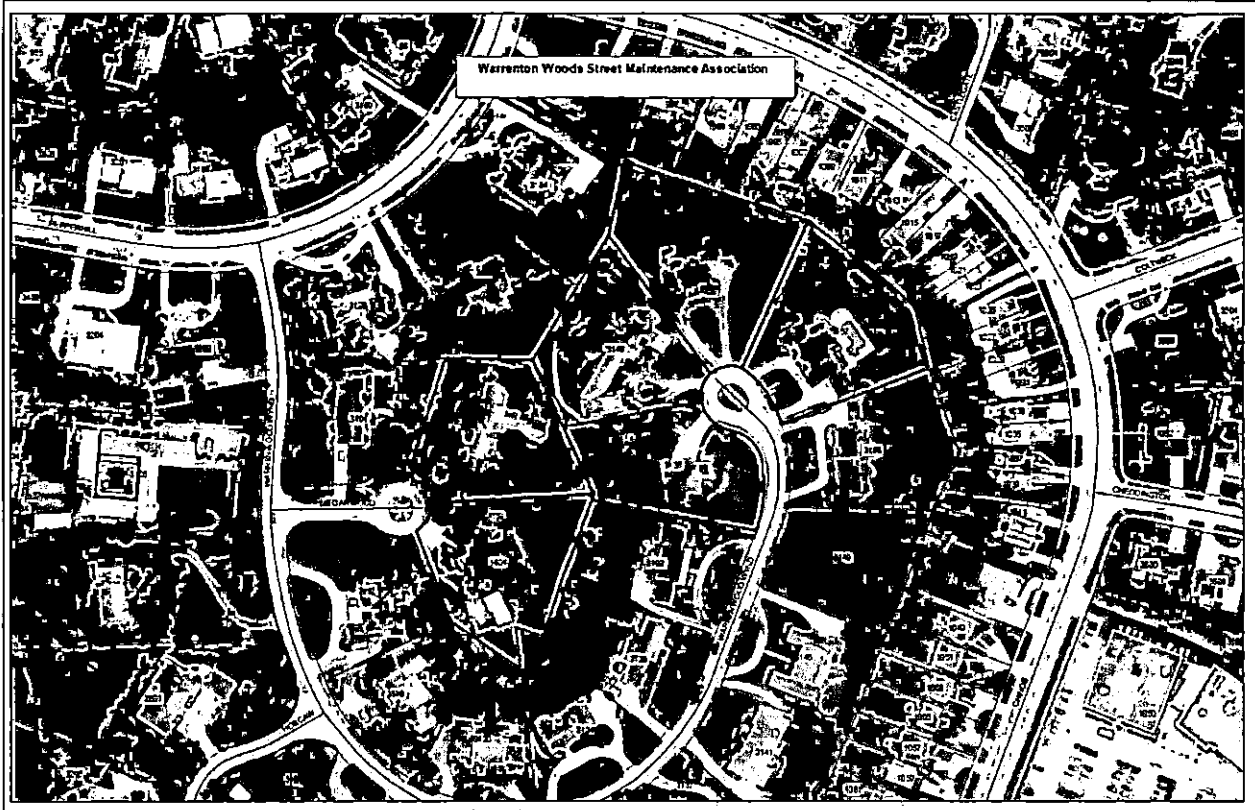


FIGURE 2 – PROJECT AREA - WWSMA STORMWATER SWALE REMEDIATION

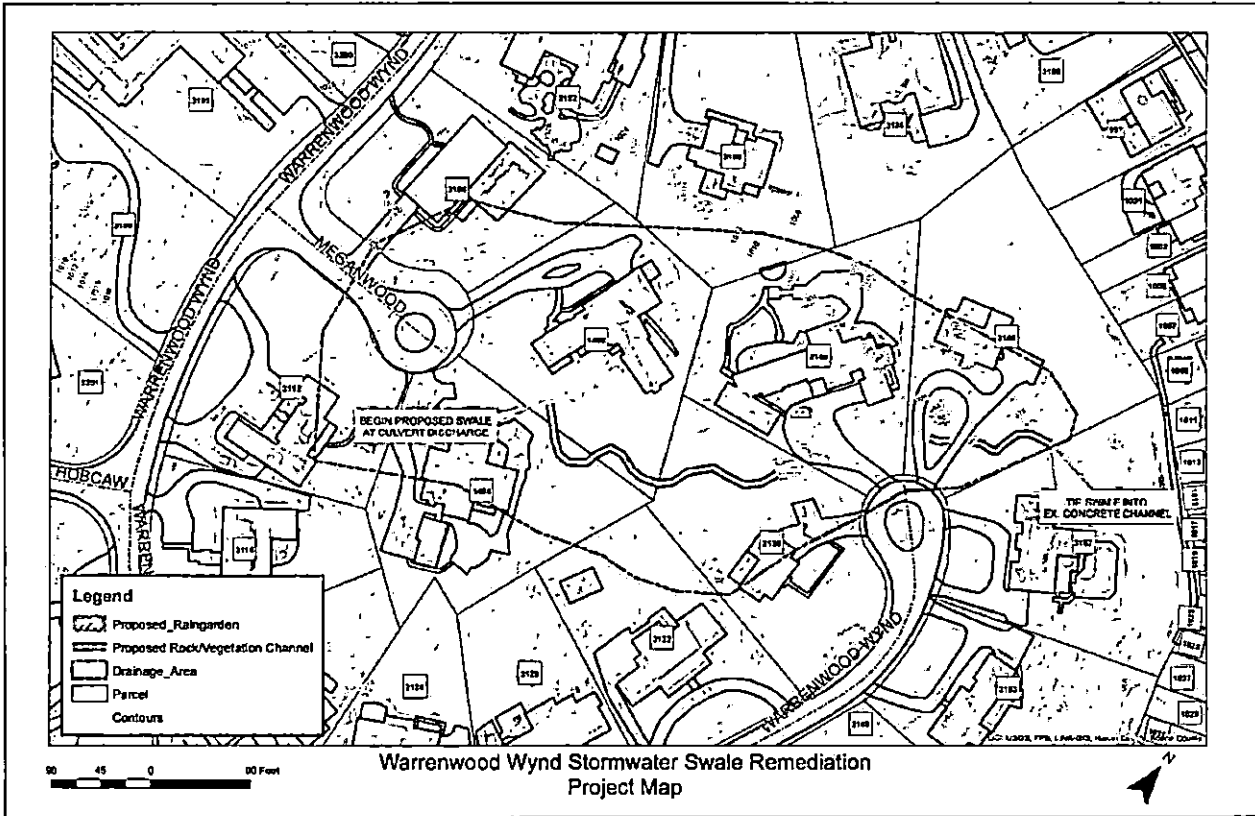

GRANT AWARD AGREEMENT


Fiscal Year 2020 Class A Incentive Grant Program

THIS AGREEMENT, made and entered into on the 6th day of March, 2020, by and between the LEXINGTON-FAYETTE URBAN COUNTY GOVERNMENT, an urban county government of the Commonwealth of Kentucky, pursuant to

(HO)

(DPS)

Stormwater Quality Projects Incentive Grant Program

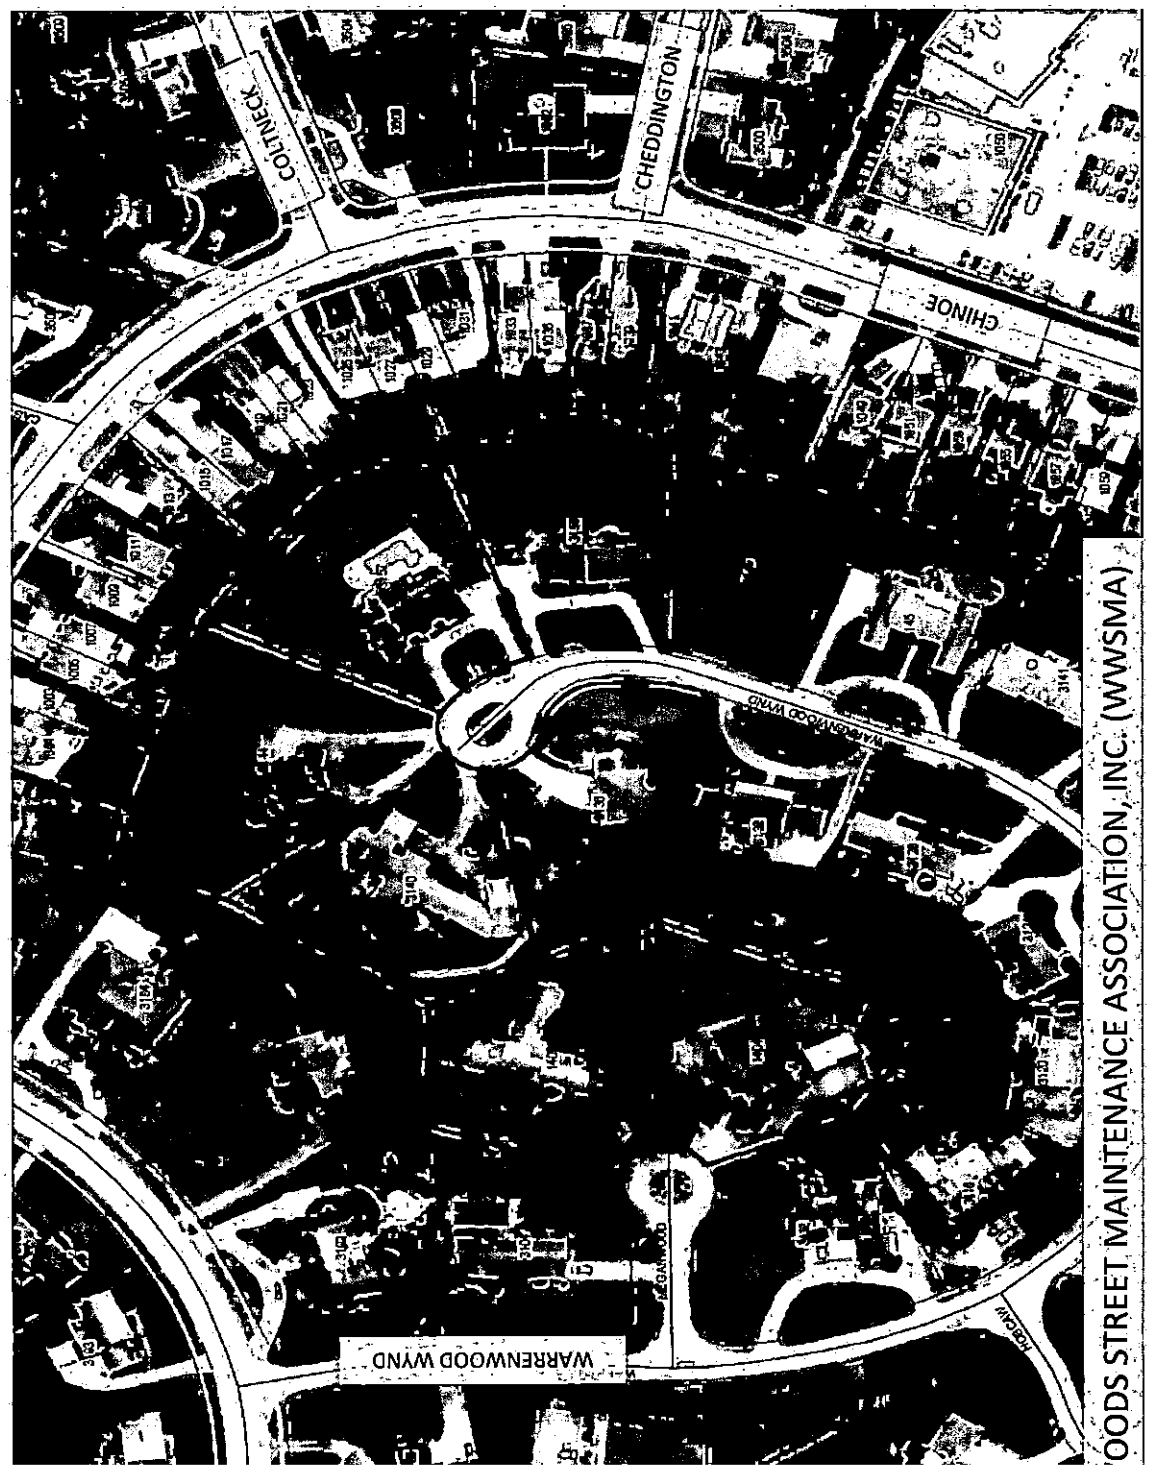

WOODS STREET MAINTENANCE ASSOCIATION, INC. (WWSMA)

(5) The Grant to the Grantee shall be disbursed in the following manner:

- (a) The Grantee shall submit, at least once every three (3) months, a *Grant Reimbursement Form* and a *Request for Funds*, in standardized format provided by the Government, to the Government's Grant Manager designated by the Director of the Division of Water Quality for the project. The *Request for Funds* shall include documentation that the Grantee has already expended the requested funds or shall be in a position to expend properly the requested funds within thirty (30) days of receipt of the funds. The *Request for Funds* shall include full accounting of all eligible grant-related expenses, as listed in Attachment A. Copies of invoices, purchase orders, or receipts showing vendor, date, amount, and items purchased or ordered shall be provided with the *Request for Funds*.
 - (b) Each *Request for Funds* shall include documentation of all of the Grantee's Match Costs listed in Attachment A and claimed for the prior period. For cash expenditures this shall include receipts, showing vendor paid, date, amount, and items purchased. For volunteer hours this shall include sign-in sheets describing the events with signatures, name, address, time in and time out (or length of event), for each participant (volunteers must be 12 years of age or older). For mileage, this shall include driver name, type of vehicle, location to and from, date, and miles driven.
 - (c) Each *Request for Funds* shall be accompanied by a *Project Status Report*, in a standardized format provided by the Government, describing the progress of the project to date, including a description and schedule of all activities completed, and hardcopy or electronic copies of materials completed and/or used to date. For educational events (if applicable), copies of the class sign-in sheets documenting the number of attendees shall be provided.
 - (d) The Government's Grant Manager shall review each *Request for Funds* and supporting documents for compliance with the terms of this Agreement and the guidelines of the Stormwater Quality Projects Incentive Grant Program. If the Government's Grant Manager finds the Grantee's *Request for Funds* is in compliance with the terms of this Agreement and the Program's guidelines and that the activity progress and management program of the Grantee satisfy the terms of this Agreement, he or she shall approve the *Request for Funds* within 15 days of receipt, and then forward it to the Division of Accounting for payment.
 - (e) Should the Government's Program Administrator determine that the Grantee is not in compliance with the terms of this Agreement and/or the Stormwater Quality Projects Incentive Grant Program, including deficiencies in progress and/or management of the project, the Division of Water Quality shall notify the Mayor's Office and the appropriate district Council person and shall meet with the Grantee on matters that prevent approval of the *Request for Funds*. Failure to resolve any such matters to the satisfaction of the Government may lead to termination of the Agreement for cause pursuant to Paragraph 25 herein below.
 - (f) The Government shall release payment of the final 3% of the Grant only after receipt and acceptance of the Project Final Report. The Government's Grant Manager shall review the Project Final Report and provide comments to the Grantee within 15 calendar days or, if acceptable, forward approval to the Division of Accounting for payment.
- (6) For any project which includes installation of permanent capital infrastructure as listed in Attachment A (not to include individual rain barrels, small rain gardens, and pond equip-

- (7) For any project which includes installation of permanent capital infrastructure as listed in Attachment A, the Grantee agrees to provide in hard copy and electronic format the following deliverables as they become available, each sealed by a Professional Engineer licensed in the Commonwealth of Kentucky (or Registered Landscape Architect when allowed by Kentucky Revised Statutes 323A.010):
- Design calculations;
 - Final construction plans, including erosion and sediment control plans, traffic control plans, grading plans, etc.;
 - Final specifications and bidding documents (if applicable);
 - Detailed engineer's construction cost estimate including quantities;
 - Inspection, Operation, and Maintenance Plan laying out the plan for regular inspection and maintenance of each proposed facility for design performance and safety in accordance with manufacturer's specifications and the Government's Stormwater Manual.
 - Copies of all federal, state, and local permits, approvals, encroachments, etc. obtained for the project.
 - Record Drawing showing all field changes, and signed and sealed by the professional of record certifying the project as shown meets all original design intent.
 - Photo documentation of site conditions and improvements before, during, and after construction.
- (8) For any project which includes installation of permanent capital infrastructure listed in Attachment A, the Grantee shall provide, by the end of the design phase, certification by a Professional Engineer or Registered Landscape Architect licensed in Kentucky that all stormwater control facilities proposed for this project are feasible and viable Best Management Practices (BMPs) for controlling stormwater quality and/or quantity and are appropriate for the project site.
- (9) The Grantee agrees that any and all stormwater control facilities, including equipment and infrastructure, constructed or purchased with Grant monies shall remain the property of the Grantee, or the current property owner, or his successors and assigns, unless otherwise noted in Attachment A.
- (10) The Grantee agrees that all stormwater control facilities, including equipment and infrastructure shall remain in service and maintained by the Grantee or its representatives for at least the Service Life listed in Attachment A. For capital infrastructure, this shall include following the Inspection, Operation, and Maintenance Plan developed for each facility referenced in Paragraph 7 above. For capital infrastructure, the Grantee further accepts and agrees to enter into the "*Agreement to Maintain Stormwater Control Facilities for Class A Incentive Grant Projects*" attached hereto as Attachment B and which is incorporated herein by reference as if fully set out herein.
- (11) The Grantee agrees, and all individual property owners with grant-funded improvements installed on their properties shall agree, to allow the Government access to perform monitoring of the project elements for compliance with this Agreement.
- (12) The Grantee agrees to comply with all applicable local, state, and federal rules, regulations, ordinances, and laws in implementation of the project.
- (13) The Grantee agrees to obtain all necessary local, state, and federal permits and approvals in a timely manner and prior to the start of any work requiring such permits or approvals.
- (14) The Grantee agrees to obtain written approval from the Government's Grant Manager or Program Administrator for any proposed changes to the Project Team or Project Plan as

ments or stipulations of this Agreement, the Government shall provide the Grantee thirty (30) calendar days to address the deficiency or violation. If the Grantee does not, after the thirty (30) days, come into compliance with this Agreement, the Government shall thereupon have the right to terminate this Agreement by giving written notice to the Grantee of such termination and specifying the effective date thereof, at least five (5) calendar days before the effective date of such termination. In that event, all finished or unfinished documents, receipts and reports prepared by the Grantee shall, at the option of the Government, become its property and the Grantee shall immediately repay to the Government all monies received pursuant to this Agreement less any amount representing just and equitable compensation for the Government's share of any satisfactory work completed pursuant to the Agreement.

- (26) The Grantee's sole remedy for a breach of this Agreement by the Government shall be limited to the amount of the Grant.

IN WITNESS WHEREOF, the parties hereto have executed this Agreement at Lexington, Fayette County, Kentucky, this the day and year first above written.

LEXINGTON-FAYETTE URBAN COUNTY
GOVERNMENT

BY: Linda Gorton
LINDA GORTON, MAYOR

ATTEST:

Blackmerzee Sommers
Deputy CLERK, URBAN COUNTY COUNCIL

Grantee Organization: ANDOVER NEIGHBORHOOD ASSOCIATION, INC.
141 PROSPEROUS PLACE, SUITE 21B
LEXINGTON, KY 40509

BY: Jacqueline S. Long
NAME: Jacqueline S. Long
TITLE: Board President

The foregoing Agreement was subscribed, sworn to and acknowledged before me by JACQUELINE S. LONG, as the duly authorized representative for and on behalf of ANDOVER, on this the 21ST day of JANUARY, 2020.
My commission expires: July 31, 2020.


NEIGHBORHOOD ASSOCIATION, INC. Edwin M. Gibson
NOTARY PUBLIC
#597924

ATTACHMENT A
to the GRANT AWARD AGREEMENT
between Lexington-Fayette Urban County Government (LFUCG) and
Andover Neighborhood Association, Inc. (ANA)

GRANT PROGRAM **FY2020 Stormwater Quality Projects Incentive Grant Program**
Class A (Neighborhood) Projects

- Funded through the LFUCG Water Quality Management Fee
- Administered by the LFUCG Division of Water Quality in the Department of Environmental Quality and Public Works

PROJECT TEAM AND CONTACT INFORMATION

Grantee Organization: Andover Neighborhood Association, Inc. (ANA)

141 Prosperous Place, Suite 21B
Lexington, KY 40509
KY Organization #0280531

Organization President: Jackie Long
859-227-7755 (phone)
jacquelineslong@gmail.com (email)

Primary Project Contact & Project Manager: Scott Lange, P.E., CFM
502-645-1227 (phone)
scott.lange@landrengineers.com (email)

Secondary Project Contact: Nicole Galavotti, P.E.
859-396-8453 (phone)
Nicole_Galavotti@shieldmw.com (email)

Project Site Location: 3700 Todds Road
PVA Parcel #38276830

Property Owners: Andover Neighborhood Association, Inc.
c/o All Points Community Management LLC
141 Prosperous Place, Suite 21B
Lexington, KY 40509

Design Engineering Firm: L&R Engineers
533 Lake Valley Drive
Lexington, KY 40509
502-645-1227 (phone)
Scott Lange, P.E. (Engineer of Record)
scott.lange@landrengineers.com (email)

Contractor: To Be Determined

PROJECT PLAN ELEMENTS

All improvements shall be located on the property at 3700 Todds Road, Lexington, KY 40509. No other property or Right-of-Way shall be disturbed without the written permission from the property owners and/or LFUCG.

The objective of this project is to design and construct solutions to address the protection of the

Government's Grant Manager or Program Administrator for any time extensions beyond the grant period. Failure to gain written approval prior to making changes may lead to termination of the Agreement for cause pursuant to Paragraph 25 herein below.

- (16) The Grantee understands that the Grant shown herein in Paragraph 1 is a not-to-exceed amount, and any additional funding needed to complete the project elements listed in Attachment A is the responsibility of the Grantee. If it becomes apparent to the Grantee or the Government that the Grantee will be unable to complete the project either in the manner or for the amount described in this Agreement, then the Grantee must immediately notify the Government's Grant Manager and Program Administrator by providing a complete and detailed written explanation of its inability to comply with the terms of the Agreement. The Grantee must further provide the Government's Grant Manager and Program Administrator with a complete and detailed written explanation of any proposed changes, and the reasons for those changes.
- (17) The Grantee asserts that it is an incorporated organization registered in active status with the Commonwealth of Kentucky Secretary of State, and is in full compliance with all applicable provisions of the Lexington-Fayette Urban County Government's Code of Ordinances Chapter 5 – Buildings and Building Regulations, Chapter 7 – Finance and Taxation, Chapter 12 – Housing, and Chapter 16 – Sewage, Garbage, Refuse, and Weeds, or in compliance with Kentucky Department of Housings Buildings and Construction rules and requirements as is appropriate for those state institutions, parcels, or buildings which are subject to state regulations and oversight as opposed to local ordinances and regulations. If the Grantee becomes out of compliance with any of these provisions, it will contact the Government's Program Administrator immediately. Failure to resolve any such matters to the satisfaction of the Government may lead to termination of the Agreement for cause pursuant to Paragraph 25 herein below.
- (18) This Agreement may not be modified except by written agreement of the Government and the Grantee.
- (19) In any advertisement of the grant-funded project, whether oral or written communications, the Grantee agrees to identify the Lexington-Fayette Urban County Government as the source of the above referenced funds; the Grantee shall not specifically identify any individual or elected official as being responsible for the funds donated by the Government.
- (20) The Grantee agrees to allow the Government to publicize the Grantee's project through the Government's website and other media.
- (21) The Grantee agrees to reference the Lexington-Fayette Urban County Government's Water Quality Management Fee and the Stormwater Quality Projects Incentive Grant Program as a source of funding for the project on any permanent signage or educational brochures, presentations, websites, etc. produced using grant monies.
- (22) The Grantee is solely responsible for assuring that adequate and appropriate insurance or other necessary coverage is maintained during the term of this Agreement.
- (23) The Grantee shall provide equal opportunity in employment as required by applicable federal, state, and local laws, regulations and ordinances.
- (24) The Government assumes no responsibility whatsoever in the Grantee's project activities. Grantee shall defend, indemnify, and hold harmless the Government from and against any and all liability, claims, damages, losses, actions, costs, expenses, obligations, fines, and assessments of whatever kind, including defense costs and attorney's fees that are in any way incidental to or connected with, or that arise or are alleged to have arisen, directly or indi-

- B. Community Stream Clean-up – Community stream clean-up extending along East Hickman Creek from Todds Road to the pond just upstream of Jacobson Reservoir.
- C. Permeable Pavers – Pervious pavers to reduce the runoff from the cart path that extends from the bridge at the former 11 and 12 bridge.
- D. Stormwater education – Stormwater education through permanent signage at the proposed bank stabilization location explaining the benefits of riparian buffers. Educational pamphlets will be both mailed and emailed to residents on understanding the importance of water quality and the reduction of stormwater runoff.

2) **DESIGN:**

No grant-funded activities shall occur until the LFUCG Grant Manager gives notice-to-proceed, in writing, for the start of the design phase of the project.

Design tasks will include meetings, survey, engineering design, permit submittals to the applicable local, state, and federal agencies, bidding, and construction.

Design shall also account for the following stipulations:

- Submittals for stream permits (401/404) shall be completed as early as possible in the design process to inform the Design Engineer of alternatives that can be permitted without triggering state or federal mitigation requirements (if required).
- The Design Engineer shall meet with the LFUCG Grant Manager for at least three meetings during the design phase:
 - i) Prior to the start of design
 - ii) At the completion of approximately 50% design
 - iii) At the 95% completion of the design documents

The Design Engineer shall provide a copy of the preliminary plans (working drawings), calculations, and specifications (if available) representing 50% and 95% completion. These submittals shall be used to assist LFUCG staff in understanding the project components and allow for feedback to ensure the Government's funds shall be utilized for sustainable and effective infrastructure.

- All existing utilities shall be located and shown on the design plans.
- All existing easements, adjacent property lines, and Rights-of-Way shall be shown on the design plans. If any work is proposed to occur within any easement (i.e., utility, etc.), whether public or private, the Organization shall obtain all necessary encroachment agreements from the authorized agencies prior to the start of construction.
- Any work proposed within or on public right-of-way, easement, or LFUCG-owned property will require one or more permits or approvals. This includes installation permits for connection into any existing curb inlet or stormwater manhole located within public right-of-way. Please contact the appropriate staff:

Environmental Services (street trees), Tim Queary – tqueary@lexingtonky.gov
 Engineering (right-of-way), Brian Knapp – bknapp@lexingtonky.gov
 Sanitary Sewers, Rod Chervus – rchervus@lexingtonky.gov
 Stormwater, Greg Lubeck – glubeck@lexingtonky.gov

- Erosion and sediment control and traffic control measures shall be designed to meet all standards and follow guidelines in the LFUCG Engineering Manuals, and shall be shown on the design plans with appropriate notes.

3) **CONSTRUCTION:**

Facilities shall be constructed per the design plans and specifications. Construction of the proposed facilities shall also meet the following stipulations:

- **No construction shall occur until written approval from all affected property owners is provided to the LFUCG Grant Manager.**
- Construction shall not begin until all permits, approvals, agreements, etc. are obtained and copies provided to the LFUCG Grant Manager.
- All existing utilities shall be contacted, located, and coordinated with prior to any work being performed.
- The Erosion and Sediment Control Plan shall be provided to LFUCG for review and comment. The LFUCG Land Disturbance Permit shall be obtained by the contractor after placement of the ESC and traffic control measures.
- Failure to place acceptable erosion and sediment control measures into service prior to start of construction will result in shut-down of the job site until the measures are put in place. Construction practices shall be put in place to prevent the illicit discharge of sediment, dirt, sand, fluids, trash, and any other pollutant into the Municipal Separate Storm Sewer System or Waters of the Commonwealth.
- The Organization shall host a pre-construction meeting with all parties. The LFUCG Grant Manager shall be invited to this meeting and given 3 business days notice.
- The Organization is responsible to provide all construction oversight, administration, and daily inspection. LFUCG shall not provide these services.
- The Organization shall document construction by taking before, during, and after photographs.
- Once construction is complete, a final walk-thru inspection shall be performed. The LFUCG Grant Manager shall be invited to this inspection and given 5 business days notice. If punch-list items are identified, a second inspection shall be performed once those items are resolved, and the LFUCG Grant Manager shall be invited to this inspection and given 5 business days notice.
- The Organization agrees to enter into the *Agreement to Maintain Stormwater Control Facilities for Class A Incentive Grant Projects* included as Attachment B of the Grant Award Agreement within 21 calendar days of the final (post punch-list) inspection. This Agreement may be recorded by LFUCG at the Fayette County Clerk's office.

REPORTING REQUIREMENTS

- 1) At the completion of the Design Phase, the Organization shall provide the LFUCG Grant Manager three (3) hard copies and one (1) digital copy each of the following six (6) deliverables, each sealed by a professional licensed to perform such work in accordance with Kentucky Revised Statutes (KRS):

- Inspection, Operation, and Maintenance Plan laying out the plan for regular inspection and maintenance of each proposed facility for design performance and safety in accordance with manufacturer's specifications and LFUCG's Stormwater Manual
- 2) The Organization shall allow LFUCG twenty-one (21) calendar days to review the submittals and provide comments. If revised submittals are required, the Organization shall allow LFUCG ten (10) calendar days for review per submittal. LFUCG may choose to have a third party engineering consultant assist LFUCG in review of these submittals.
 - 3) **The design phase shall end when the LFUCG Grant Manager provides written acceptance of the design submittals.**
 - 4) If the project is to be competitively bid, the selected contractor's unit price contract/bid list shall be provided to the LFUCG Grant Manager prior to the start of construction.
 - 5) If the project is not competitively bid, the selected contractor's unit price contract shall be provided to the LFUCG Grant Manager prior to the start of construction, along with a justification for any derivations from the engineer's construction cost estimate.
 - 6) The Organization shall submit copies of all required local, state, or federal permits, approvals, public or private encroachment agreements, etc. to the LFUCG Grant Manager prior to the start of construction.
 - 7) Copies of written approval/agreement from affected property owners shall be provided to the LFUCG Grant Manager prior to proceeding with construction.
 - 8) **The construction phase shall begin only after the LFUCG Grant Manager gives notice-to-proceed, in writing, for the start of the construction phase of the project.**
 - 9) If, during construction, the contractor requests a deviation or addition to the quantities or costs in the construction contract, the LFUCG Grant Manager shall be notified within 2 business days. Additions or modifications to the project that are not directly related to the intended and correct function of the stormwater control project elements as described in the Project Plan Elements listed above and in original incentive grant application are not eligible for Grant reimbursement. Therefore, the Organization is advised that it should coordinate closely with the LFUCG Grant Manager during construction to ensure the work being performed is in compliance with this Agreement. Note that per the Grant Award Agreement all over-runs that result in the project costs exceeding the Grant amount are the responsibility of the Organization.
 - 10) After construction is completed, the Project Final Report shall include copies of the following:
 - Summary of final construction costs and quantities
 - Copies of all federal, state, and local permits obtained for the project (if not previously provided)
 - 3 copies of a Record Drawing showing all field changes, and signed and sealed by the professional of record certifying the project as shown meets all original design intent
 - Copies of final inspection minutes, punchlists, etc.
 - Photo documentation of site conditions and improvements before, during, and after construction
 - Signed *Agreement to Maintain Stormwater Facilities Funded by an LFUCG Stormwater Quality Projects Class A Incentive Grant* (Note: This form will be completed after construction is completed and final costs determined.)
 - 11) LFUCG shall make final payment of the 3% retainer after acceptance of the Project Final Report.

- B. Signage: Stormwater education through permanent signage at the proposed bank stabilization location explaining the benefits of riparian buffers.
- C. Pamphlets: Educational pamphlets will be both mailed and emailed to residents on understanding the importance of water quality, and the reduction of stormwater runoff.

PERMANENT FACILITIES / INFRASTRUCTURE

Permanent Capital Infrastructure: This grant does include Permanent Capital Infrastructure for purposes of the Grant Award Agreement.

Ownership: The proposed permanent facilities are expected to reside on private property in Fayette County and be owned by the property owners.

Future Inspection and Maintenance: The Organization (and/or Property Owner) agrees to sign and abide by the terms of the *Maintenance Agreement for Stormwater Control Facilities for Class A Incentive Grant Projects* included as Attachment B to the Grant Award Agreement. At the end of construction, the Organization may choose to: a) enter into the Agreement with LFUCG and assume responsibility for maintenance or b) enter into the Agreement with LFUCG for responsibility to ensure maintenance, and enter into a second private agreement with the property owners to perform the future maintenance.

Monitoring by LFUCG: The Organization agrees to allow LFUCG staff future access to any property on which work is performed to monitor the installed features for compliance with this Agreement following the grant period. After the grant period has ended, the Organization agrees to allow LFUCG access for monitoring per the terms of the Maintenance Agreement. Water quality sampling via grab samples or other methods may be employed by LFUCG staff as part of LFUCG's annual reporting requirement of its Kentucky Pollutant Discharge Elimination System (KPDES) MS4 Phase 1 Permit.

GRANT PERIOD & PROJECT SCHEDULE

The grant period starts on the date of execution by the Mayor and extends for the time period as listed in the Grant Award Agreement. Any time extensions must be approved in writing by the LFUCG Grant Manager. The project schedule shown in Table 1 is preliminary. Proposed changes to the project which alter this schedule significantly shall be discussed with the LFUCG Grant Manager prior to implementation.

TABLE 1 – PRELIMINARY PROJECT SCHEDULE

Activity	Anticipated Date(s)
Notice to Proceed	February 2020
Permitting	February 2020 – August 2020
Design	February 2020 – April 2020
Construction Inspection	September 2020 – October 2020
Construction	September 2020 – October 2020
Clean-up Day	August 2020
Permanent Signage	December 2020
Project Closeout / Final Report to LFUCG	January 2021 – March 2021

ADDITIONAL GRANT STIPULATIONS

1. Organization shall verify the need and ensure all permits are received (i.e., FEMA, Army Corps, DOW, etc.) prior to any bank stabilization work.

4. Organization proposes a larger cost share beyond that required by the grant program. Budget shall reflect the 21% cost share offered in the application (approximately \$19,474.10).

PROJECT BUDGET – GRANT ELIGIBLE EXPENSES

Table 2 lists the Eligible Expenses for the design and construction phases of this project. Only properly invoiced items shall be reimbursed with grant monies or counted toward the Organization’s cost share.

Any work performed on this project prior to grant award by Urban County Council and Notice-to-Proceed from the LFUCG Grant Administrator is NOT an eligible expense and shall not be reimbursed or counted toward the cost share.

The construction estimate will be revised as part of the design process. The Grant is a not-to-exceed amount, and any cost overruns are the responsibility of the Grantee.


TABLE 2 – PROJECT BUDGET

	Type of Expense	Participants	Item	Unit Price	Quantity	Funded by Organization	Funded by Grant	Total Expense
1 Grant Management								
2	Donated	Grant Manager	Grant Management	\$14.87 per hour	20	297.40	-	297.40
3 Bank Stabilization								
4	Donated Consulting Fees	Engineer	Permitting	\$38.23 per hour	60	2,293.80	-	2,293.80
5	Donated Consulting Fees	Engineer	Engineering Design	\$38.23 per hour	60	2,293.80	-	2,293.80
6	Donated Consulting Fees	Engineer	Construction Inspection	\$38.23 per hour	40	1,529.20	-	1,529.20
7	Donated Consulting Fees	Biologist	Native Plantings Design	\$15.00 per hour	12	180.00	-	180.00
8	Labor	HOA Volunteers	Haul	\$23.00 ton	310	7,130.00	-	7,130.00
9	Labor	Contractor	Excavation	\$38.00 cuyd	230	-	8,740.00	8,740.00
10	Labor	Contractor	Remove Pavement	\$7.80 sqyd	98	-	764.40	764.40
11	Labor	Contractor	Remove Retaining Wall	\$56.20 lf	115	-	6,463.00	6,463.00
12	Materials	HOA/Contractor	Channel Lining Class II	\$39.60 ton	84	3,326.40	-	-
13	Materials	HOA/Contractor	Channel Lining Class II	\$39.60 ton	100	-	3,960.00	7,286.40
14	Materials	Contractor	Crushed Stone Base	\$27.30 ton	18	-	491.40	491.40
15	Labor	Contractor	Remove Stone Baskets	\$56.20 lf	75	-	4,215.00	4,215.00
16	Materials	Contractor	Pervious Pavers	\$18.00 sqft	890	-	16,020.00	16,020.00
17	Materials	Contractor	Trees	\$400.00 each	7	-	2,800.00	2,800.00
18	Materials	Contractor	Shrubs	\$250.00 each	3	-	750.00	750.00
19	Materials	Contractor	Top Soil	\$37.90 cuyd	310	-	11,749.00	11,749.00
20	Materials	Contractor	Native Plantings	\$1.00 sqyd	1260	-	1,260.00	1,260.00
21	Materials	Contractor	Silt Fence	\$4.50 lf	330	-	1,485.00	1,485.00
22	Materials	Contractor	8% General Conditions	\$5,532.34 each	1	-	5,532.34	5,532.34
23	Fee	Engineer	Stormwater Permitting Fees	\$100.00 each	1	100.00	-	100.00
24	Labor	Contractor	10% Contingency	\$7,545.10 each	1	-	7,545.10	7,545.10
25 Stream Cleaning and Educational Outreach								
26	Stream Clean-up	HOA Volunteers	Stream Clean-up	\$7.25 per hour	150	1,087.50	-	1,087.50
27	Supplies	HOA Board	Work Gloves	\$6.00 per pair	20	120.00	-	120.00
28	Supplies	HOA Board	Trash Bags	\$5.00 per box	10	50.00	-	50.00
29	Materials	HOA Board	Educational Pamphlet	\$0.75 each	1400	1,050.00	-	1,050.00
30	Labor	HOA Volunteers	Educational Pamphlet Mailing	\$7.25 per hour	16	116.00	-	116.00
31	Materials	HOA Board	Permanent Signage	\$500.00 per sign	3	-	1,500.00	1,500.00

FIGURE 1 – ANA SITE PLAN (FROM APPLICATION)



FIGURE 2 – ANA MAP OF PROJECT AREA

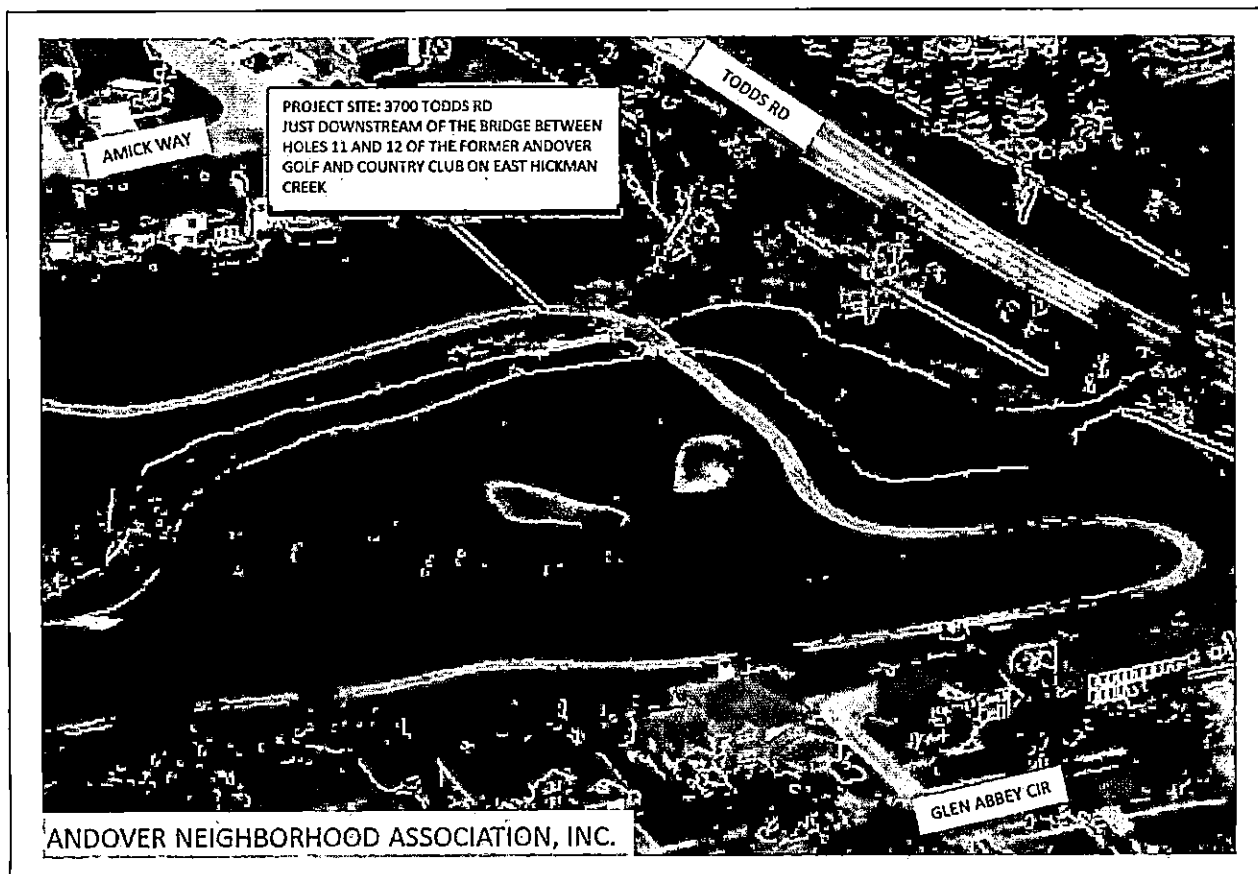

Stormwater Quality Projects Incentive Grant Program

