



**Architectural and
Engineering Services
for
Castlewood Community
Center
Renovation**

#56-2015

**Lexington
Fayette
Urban
County
Government
Parks and
Recreation
Department**

FITZSIMONS OFFICE OF ARCHITECTURE, INC.

112 West Third St. Lexington, KY 40508-1700

fax 859●226●9283

tel 859●243●0838

Maple Ave

Burnett Ave

Avon Ave

Burnett Ave

Arceuth Ave

December 22, 2015

Mr. Todd Stalin
Purchasing Director
LFUCG
200 West Main Street
Lexington, KY 40507



FITZSIMONS OFFICE of ARCHITECTURE, INC.

112 W. Third St. Lexington, KY 40508-1700

tel 859●243●0838

fax 859●226●9283

56-2015 Castlewood Community Center Renovation

1. Estimated Cost of Services

Phase I

Investigation

- On site visits
- Selective demolition and repair back

Document existing building with base plans (use owner provided plans)

- Photograph existing conditions
- Site Plan, either based on owner provided engineered survey (or a less accurate but usable site plan based on measurements and site photographs)
- Plans; Site, Foundation, 1st, Roof, HVAC, Plumbing, Electric
- Elevations, Exterior
- Sections, Building Sections (2), one in each direction Programming/Community Meetings
- Schematic Design Phase
- Cost Estimates

Phase I Total (see attached Form of Proposal next page)


\$18,000

Phase II

- Construction Documents **(see attached Form of Proposal, next page)**
- Construction Administration **(see attached Form of Proposal, next page)**

Hourly Rates

Principal Architect/Engineer	\$175
Project Manager Architect/Engineer	\$125
Architect/Engineer Staff	\$ 85
Non-professional Staff	\$ 55

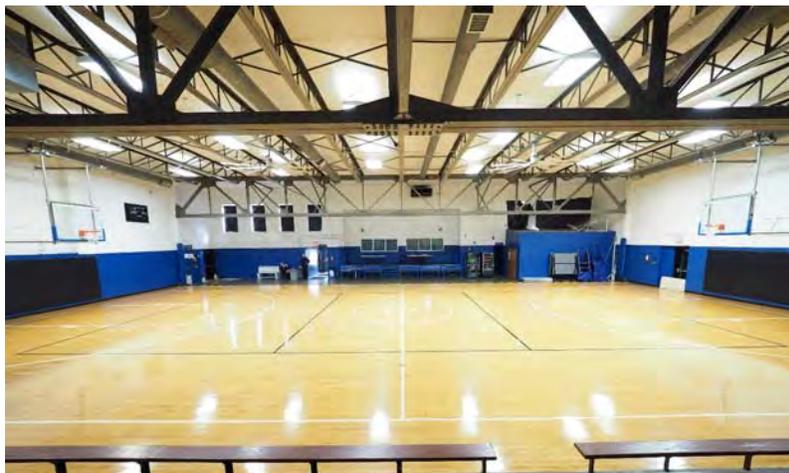

Form of Proposal

Phase I Design Services		Lump Sum Fee
1. Site Plan & Existing Building Plan/Report		\$ 5,000
2. Program Development & Schematic Plans		\$ 8,600
	50% Schematic Design \$5,600	\$ -
	100% Schematic Design \$3,000	\$ -
3. Phasing Recommendations & Cost Estimates		\$ 4,400
Total		\$ 18,000

Phase II Design Services **Fee in Percent of %
of Construction
Budget**

4. Construction Documents		
Budget for Construction	\$100,000 and under \$200,000	8.6%
	\$200,000 and under \$300,000	8.0%
	\$300,000 and under \$400,000	7.5%
	\$400,000 and under \$500,000	7.2%
	\$500,000 and under \$600,000	7.0%
5. Construction Administration		
Budget for Construction	\$100,000 and under \$200,000	2.2%
	\$200,000 and under \$300,000	2.0%
	\$300,000 and under \$400,000	1.9%
	\$400,000 and under \$500,000	1.8%
	\$500,000 and under \$600,000	1.7%

Hourly Rates - please attach schedule of hourly rates for any unanticipated, additional work

Principal Architect/Engineer	\$	175.00
Project Manager Architect/Engineer	\$	125.00
Architect/Engineer Staff	\$	85.00
Non-professional Staff	\$	55.00

2. Specialized Experience and Technical Competence:

The scope of services outlined for Phase I will be performed by Fitzsimons Office of Architecture (FOA), Pyramid Structural Engineers and ShROUT Tate Wilson (STW) Greg Fitzsimons; architect and team leader would be working with Whitney Casey, Cory Sharrad and Jim Smith with STW Engineering for mechanical and electrical building systems. Carman will provide landscaped design and civil engineering for any proposed site improvements. To evaluate the existing structure and envelope Mohammad Sheraji, Pyramid Engineers would inspect and document the conditions with Greg. These four firms have many completed projects similar to this between them. The architect and engineers on this project are all working project managers that basically perform all the research/design work with the assistance of staff to complete the Phase 1 Schematic Design/Existing Conditions.

Greg Fitzsimons, and FOA have worked on more than twenty community center projects in buildings of this age (1930s-1970s) and type (solid masonry, wood/steel frame). Many have been schools converted to community centers, which requires more work than Castlewood which was built as a community center.



As the historic architect for the Loudoun House renovation in 2000, part of that project included working with the neighborhood association and Art League board members to include those stake holders in the programming and decision making. This project is a great opportunity to work with the North Limestone CDC in support of the larger community efforts for a live/work/walk neighborhood. Like the neighborhood surrounding the Carver Community Center there are new interests and program needs from the changing population putting pressure on the aged existing facilities. Greg has been on the site for Art League events over the years and is more than familiar with the existing conditions at the Castlewood Center.

As part of the 2000 renovation of Loudoun a site improvement plan for the Castlewood Park including a new Community Center was developed. Many of the site improvements included in the proposed plan have been made in recent years, including the playground. Carman was part of the larger planning efforts in 2000 as well as the landscape architect and civil engineer for the site improvements.

This project team has had plenty of project experience with related projects. For LFUCG departments we are working at the Black and Williams Center, Carver Center, ArtsPlace, and Carnegie Center. These projects involve rest room renovations, window replacements, ADA access, roof, HVAC and other work similar to the building needs at Castlewood Center. Our recent bid and constructed projects provide a reasonable basis for estimating costs for the renovation. Most of our projects do not have enough funds to cover all the work needed.



The construction cost estimates are used to determine the scope of construction described in the bid documents. The project team is able to use current unit pricing to project the cost for the major divisions of work such as the roof, windows, doors, masonry, mechanical, and electrical.

With LFUCG Purchasing and Council procedures there is limited ability to use change orders to manage unforeseen conditions of renovation projects. FOA and team use our experience with similar buildings and sites to investigate the existing conditions and make practical recommendations to repair/renovate as needed.

The Lexington Fire Department has been renovating their rest rooms, roofs and site aprons as part of a several year plan to catch up on deferred maintenance. Like Parks and other City departments the last few years's budgets have provided more funds for facilities needs that have been put off for too long. LFD has used FOA for the last few years for all types of renovations and repairs including the replacement training tower on old Frankfort Pike. Our wide range of experience as well as the ability to work on unusual projects has proven quite useful. Like firemen the project team professionals get into all the details and work on all aspects of their projects.

In addition to LFUCG, FOA has provided renovation design services to other institutional clients. FOA has completed similar renovation projects, limited and extensive, for the Commonwealth, National Park Service, Municipal Governments and Fiscal Courts, School Districts numerous community groups throughout central Kentucky. In the last five years we have worked on community centers in Olive Hill, Sharpsburg, Lebanon, Mt. Sterling, Maysville, and Halderman.



Loudoun House, Morton House and Bell Place, three of the most significant historic residences in central Kentucky are FOA projects. We have been selected to work on some of our most important historic resources because of our experience in historic preservation. Yet we also tackle the less glamorous projects as replacing windows at Black and Williams or renovating R.H. Williams Cultural Center, just as significant for the building (and us) but may be not to the public. We have been fortunate to learn from these historic resources while working on them. Each building is significant to the user. We appreciate the opportunity to add to the history of each building.

FOA has worked with Parks and Recreation on these projects:


- Loudoun House
- Bell House Exit Stairs
- Gratz Park Kitchen
- Gratz Park Fountain
- Bell Carriage House ADA Ramp
- Carver Community Center Renovation, Phased Rest Rooms
- Dunbar Community Center Stone Arch Repairs
- Bell House Condition Report

For LFUCG General Services; the following:

- Morton House Repairs and Roof Replacement
- R.H. Williams Cultural Center
- LFUCG Government Building Entry Canopy
- Phoenix Building Roof Replacement
- ArtsPlace Window Replacement
- Black and Williams Window Replacement
- Carnegie Center Exterior Stone Stairs Replacement

Lexington Fire Department; the following

- Rest Room Renovations: Fire Station #1, #5, #11, #13, #14, #15
- Training Center Rest Room Renovation
- Training Tower Foundation and Pre-Engineered Structure
- Maintenance Building (new construction)
- Exit Stairs: Fire Station #3, #5
- Roof Replacement: Fire Stations #11, #15, #5, #6, #13

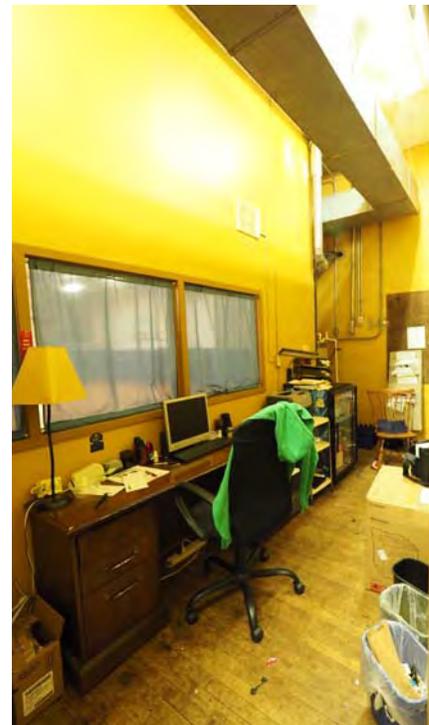

Site Improvements: #3, #6, #9, #17

Most historic building problems are related to water in all forms, getting into the building envelope. The Castlewood Center, built in the 1930's, was constructed with good materials. The design has some built-in maintenance issues yet the original materials have held up. These buildings were constructed to last of good materials. Pyramid and FOA worked on other large masonry bearing structures in central Kentucky, Bourbon County Courthouse, LFUCG Government Building, St. Peter and Paul School, Carver Community Center, including structural solutions to significant existing building issues for each.

Over time heavy masonry buildings "grow" at their top. Dormers and chimneys expand and lean. Parapet walls swell. Sometimes the building elements can be repaired in place, in other cases the masonry elements need to be rebuilt.

It is second nature for the project team members to walk into a building for the first time noting all the potential building problems. For us this one of the best, most practical ways to learn what construction detail works in our environment and what details fail. All buildings move, with different parts at different rates. Add moisture to any part, or modify it in an unforeseen way and the designed-in movement changes. Some symptoms are visible and some are not. Castlewood Center has enough visible symptoms to point to the probable causes that need to be renovated.



Castlewood Center is fairly good condition with regular repairs and maintenance to keep the building in operation. As with most buildings of this construction date, history and institutional use, it is in need of a full renovation. The more divisions of work that can be included in a general construction project the better the value for the owner. Twenty percent of the cost of a construction project goes to overhead in starting and closing-out the work.

Attached are project data sheets which demonstrate our specialized experience and technical competence with large masonry/wood framed structures. Firm information for Carman, STW and Pyramid including resumes and related project experience follow the FOA information.

3. Capacity to Perform the Work

FOA and team members will be the principal investigators on site as well as the designers for the renovation schematic. FOA, Carman, STW and Pyramid can complete Phase 1 in thirty days after the owner/user/architect programming meetings. The project team can meet the project deadlines. Once we have the existing building computerized we can quickly develop cost estimates for the divisions of construction based on current unit prices from similar projects. We are familiar with LFUCG Purchasing requirements and time table for processing a typical construction project. In the last five years FOA has bid more than twenty-five mostly small construction projects for Urban County Government.



4. Past Record of Performance

LFUCG Parks and Recreation and General Services have hired FOA and this project team on the projects mentioned above and represented in the data sheets. We believe the past consultations with LFUCG, Parks and historic renovation projects across central Kentucky have defined our character, integrity and reputation for successfully completing rehabilitation projects. It is our judgment that we work on to make it be specific for each project. The Carver Community Center is a good indicator of the project team's ability to manage a limited scope renovation, planned in phases without enough money to meet all the needs. The same individuals will be involved in this project. The roof, windows, doors and HVAC work were completed in the first phase.

The budgeted contingency funds were not needed for construction. The contingency funded the renovation of the interior finishes, greatly improving the final project. Currently the first phase of the restroom renovations is under construction. So far each phase of construction has been done for the funds available.


5. Familiarity with Details of Project

The center lacks some viability/identity even though it is part of the important historic site. There is limited signage and the entrances are not as inviting as they might be. FOA has worked on two projects on the site in the past. The 2000 Save America's Treasures Grant funded, Loudoun renovation was the major project. FOA has consulted on additional interior repairs due to drainage backups. Part of the planning services during the \$1.3 million dollar renovation in 2000, included the possibility that the Art League would take over the existing community center and a new one would be constructed. We have been familiar with the existing conditions since measuring and drawing the existing community center plans fifteen years ago. During the 2000 renovation programming and planning activities included members of the neighborhood association. Some of those same individuals are still active in community affairs and we look forward to working with them again.


6. Degree of Local Employment

All architects, engineers and staff members will be 100% local to Lexington.

Respectfully submitted,



Gregory Fitzsimons
C: file

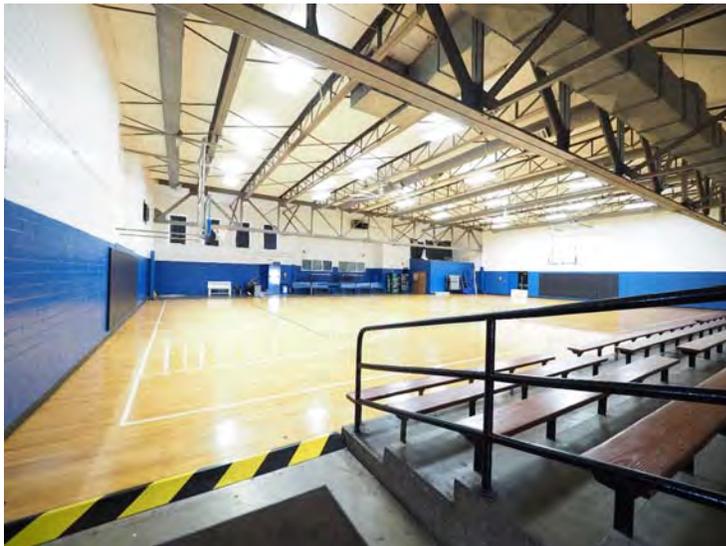

Gregory Fitzsimons, AIA
Fitzsimons Office of Architecture, Inc.



Professional and Civic Organizations

Gregory Fitzsimons started the firm of Fitzsimons Office of Architecture, Inc. in 1995 to continue his practice of modern and historic architecture. Between 1992 and 1975 Greg was a founding partner in Tate/Fitzsimons/Architects/Inc. From 1992 to 1995 he was an associate with Omni Architects. Mr. Fitzsimons has been practicing for more than thirty years. He prefers to work in a small practice in order to manage and be part of the production of each project. His first energy conscience building was a passive/active solar childcare center constructed in 1981. LEED design guidelines and efficiency in building design and construction have been considered in every project, the owner does not have to make it a priority.

American Institute of Architects
 East Kentucky Chapter
 Kentucky Society of Architects
 Blue Grass Trust for Historic Preservation
 Past President, 1989-1990

Registrations: Architect: Kentucky, 1980

Education: Bachelor of Architecture, University of Kentucky, 1975
 Honors Recipient

Professional Experience		
Carver Community Center Renovation Rest Rooms		2014
LFUCG, Lexington, KY		
Morton House Renovation		2014
LFUCG and The Nest, Lexington, KY		
Phoenix Building Roof Replacement		2013
LFUCG, Lexington, KY		
Sharpsburg Community Center and Library		2013
LFUCG, Lexington, KY		
Gratz Park Fountain Restoration		2014
LFUCG, Lexington, KY		
Lexington Fire Stations #5 & #6 Renovations		2012
LFUCG, Lexington, KY		
Sts. Peter and Paul School Renovation/Addition		2010
Diocese of Lexington, KY		
Center Square: old Lebanon Jr. and Senior High Schools		2009
City of Lebanon, Lebanon, KY		
LFUCG Government Center ADA Access		2008
Urban County Government, Lexington, KY		
Lexington Fire Station #3 Renovation		2007
LFUCG, Lexington, KY		
Kimball House Renovation Mixed Use Development		2007
Lexington, KY		
Bourbon County Courthouse Renovation		2007
Bourbon County Fiscal Court		
Springfield Opera House Renovation		2005
City of Springfield, Springfield, KY		
Loudoun House Renovation		2004
Lexington Fayette Urban County Gov., Lexington, KY		
Hopewell Museum Renovation		2004
Hopewell Museum Board, Paris, KY		
Guy Potts Building Exterior Restoration and Addition &		2004
Norsworthy Auditorium Restoration		2000
Fayette County Public Schools, Lexington, KY		
Fort Boonesborough Renovation & Gift Shop		2003
Fort Boonesborough State Park		
Commonwealth of Kentucky, Boonesborough, KY		
Fayette County Court House Renovation		2003
Lexington Fayette Urban County Gov., Lexington, KY		
Old House at Cambus-Kenneth Restoration		2002
National Trust for Historic Preservation., Washington, DC		
White Hall Sate Historic Shrine Renovation		2002
Commonwealth of Kentucky, Richmond, KY		



Carver Community Center Renovation

FITZSIMONS OFFICE of
ARCHITECTURE, INC.
112 W. Third St.
Lexington, KY 40508
859-243-0838

Carver Community Center
Renovation
Joyce Thomas
LFUCG General Services
200 East Main Street
Lexington, KY 40508
859-258-3054



Carver Community Center Renovation

The Carver Community Center is owned by the Lexington-Fayette Urban County Government and used by the Parks Department. The building was an african-american school until the 1970's when the Fayette County School System dedeed the site to LFUCG. The building has not been renovated since the school system gave up the building. In 2012 the limited renovation of the building was planned with construction to start early in 2013. The work will include a new HVAC system, VRV heat pumps with energy recovery fresh air system; a new roof; replacing non-original windows a doors with historically correct double hung windows and doors; as well as other general renovation work. FOA was able to develop a project that worked within the limited funding and accomplished the owner's major goals to make the building functional again. The budget for construction is \$1,200,000.



ArtsPlace Renovation Lexington, Kentucky

FITZSIMONS OFFICE of
ARCHITECTURE, INC.
112 W. Third St.
Lexington, KY 40508
859-243-0838

As Principal-in-Charge Tate/Fitzsimons/ Architects/Inc.

ArtsPlace renovation began with a 1903 YMCA which had been extensively modified. The Lexington Arts and Cultural Council purchased the building and renovated it for offices and studios for member groups. The existing building has a raised basement which required a two sided elevator cab to access the intermediate levels. The elevator and entry lobby installed within the existing structure created a new focal point. A sprinkler system was also installed within the existing building.

LexArts
Lexington Arts and Cultural Council
Jim Clark, President
161 North Mill Street
Lexington, Kentucky 40507




**FITZSIMONS OFFICE of
ARCHITECTURE, INC.**
112 W. Third St.
Lexington, KY 40508
859-243-0838

Sharpsburg Community Center
and Library
Dorothy Clemens, Mayor
29 Camp St.
Sharpsburg, KY 40374

**FITZSIMONS OFFICE of
ARCHITECTURE, INC.**

The city of Sharpsburg has acquired the old Sharpsburg School site and remaining WPA stone gymnasium. This Bath County community has commissioned the design and construction project that will renovate the remaining gym structure and provide a community center addition. The addition will house a library, classroom, rest rooms and mechanical space. The gym will be renovated to its original appearance including refurbishing the stage area. The restored gym will preserve and excellent example of the stone masonry used on WPA projects using Italian masons.

Sharpsburg Community Center and Library

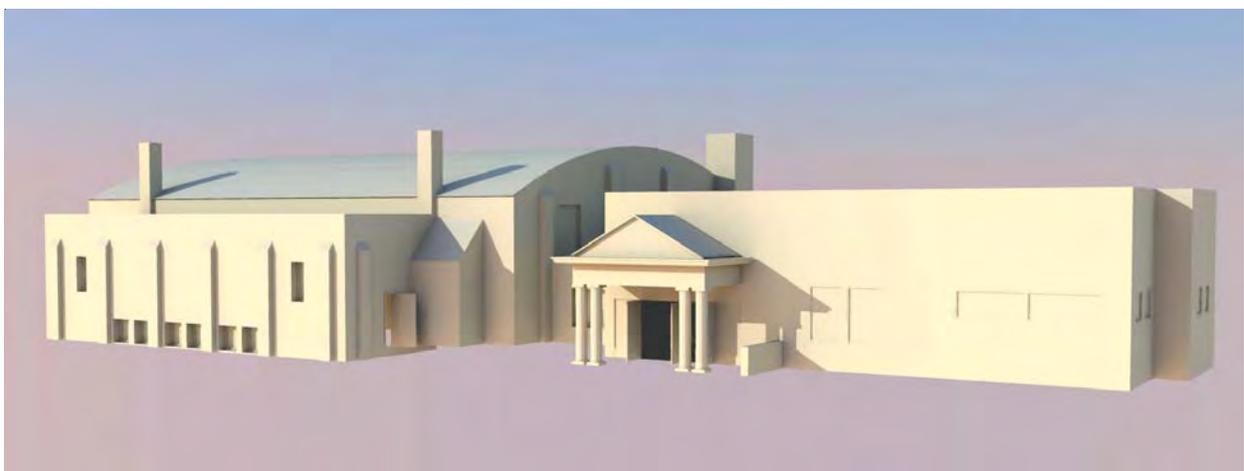

FITZSIMONS OFFICE of ARCHITECTURE, INC.
 257 N. Limestone St.
 Lexington, KY 40507
 859-243-0838

FITZSIMONS OFFICE OF ARCHITECTURE, INC.

The Urban County Government is planning the restoration of the Loudoun House as well as the conversion of the existing gym to new gallery space for the Art League. In addition a new community center is being planned to replace the existing gym.



Renovation The Loudoun House

Lexington Art League
 Lexington-Fayette Urban County
 Government



Lexington Fayette County Urban
 County Government
 Mayor Tera lassac
 Mr. Bill Carman
 Planning Parks
 Department
 Lexington, KY



WEST ELEVATION
 SCALE 1/8" = 1'-0"






Haldeman-Hayes Community Center Renovation and Addition

FITZSIMONS OFFICE of ARCHITECTURE, INC.
 112 W. Third St.
 Lexington, KY 40508
 859-243-0838

Haldeman-Hayes Community Center
 Teresa Shields
 Gateway Area Development District
 29 Camp St.
 Morehead, KY 40374

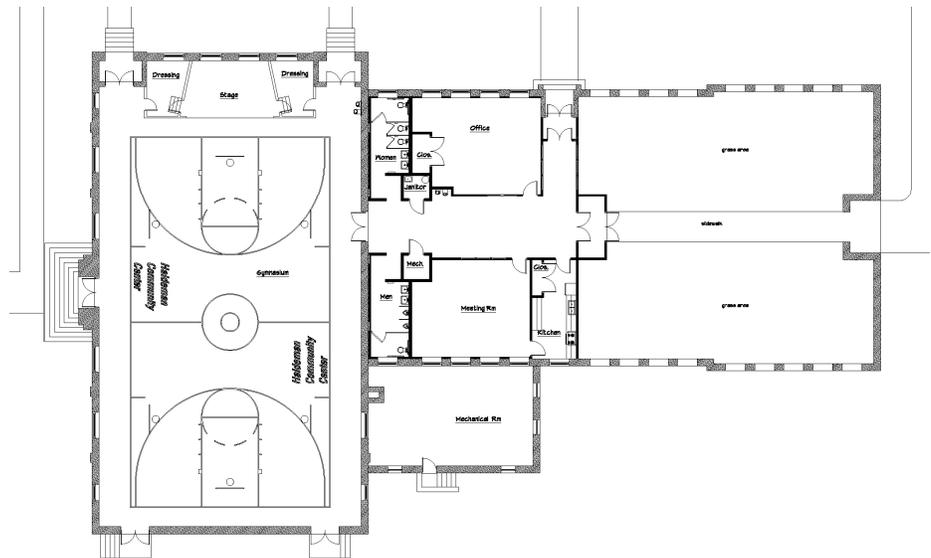

Haldeman-Hayes Community Center

In the 1930's and 1940's the area between Morehead and Haldeman included several large brick making factories that supported three to four thousand employees. Schools like the Haldeman Hayes School were constructed using WPA and CCC programs. The Haldeman school burned in 1994 destroying the classroom section while leaving the gym in tact. FOA has provided a master plan for the renovation including restoring the gym and recreating a portion of the school using the original walls. A portion of the remaining stone walls will be left as an outdoor enclosure for public events as well as a monument to the original building.



FITZSIMONS OFFICE of
ARCHITECTURE, INC.
112 W. Third St.
Lexington, KY 40508
859-243-0838

First African Foundation
William Thomas
262 Medlock Road
Lexington, KY 40517-1148

(former) First African Baptist Church Renovation and Addition

First African Foundation


(former) First African Baptist Church Renovation and Addition

The First African Baptist Church is the first African Church founded in Kentucky, the second west of the Alleghany Mountains and the third in the United States. It was constructed in 1850 by slaves for their own use. The congregation founded in 1790 provided a base for the spiritual teachings that encouraged the eventual emancipation changing the Commonwealth for the better. The pastors of this congregation, have been influential in the cultural throughout the Commonwealth including, Rev. Peter Durrett, Rev. London Ferrell, Rev. William J. Simmons and Rev. S. E. Smith. Rev. London Ferrell, who died in 1854, baptized over 5,000 people and he was honored at his funeral attended by thousands which was said to be larger than the funeral for Henry Clay.


FOA has completed a Condition Assessment Report and a schematic design for the renovation and addition to the existing structures. Unfortunately the original interior of the sanctuary was demolished in the past, but it presents the opportunity to create a sympathetic modern interior to complement and contrast the historic structure. Funding for a facility to house classical music performance hall, library, computer laboratory, history and revolving gallery space as well as community development spaces is under way. Anticipated construction budget is six to seven million dollars. 2014 is the target date to start construction.



Cardome Academy Master Plan Adaptive Reuse and Renovation

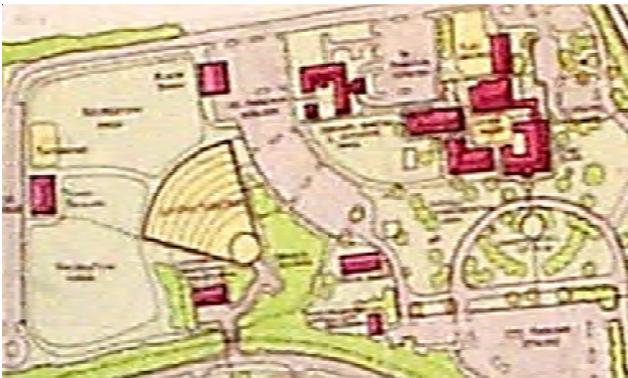

Fitzsimons Office of Architecture and John L. Carmen and Associates are working with the City of Georgetown on a Master Plan for the renovation and reuse of the ten existing building and site. The renovation to the main building includes new meeting and training rooms as well as a food service kitchen. The large performance space will be renovated for improved acoustics and other changes. New uses are planned for other buildings including a senior citizens center, adult education, child care and other community functions. The site is being designed to create a campus with improved access, parking and other site improvements. Locations for additional buildings have been established.

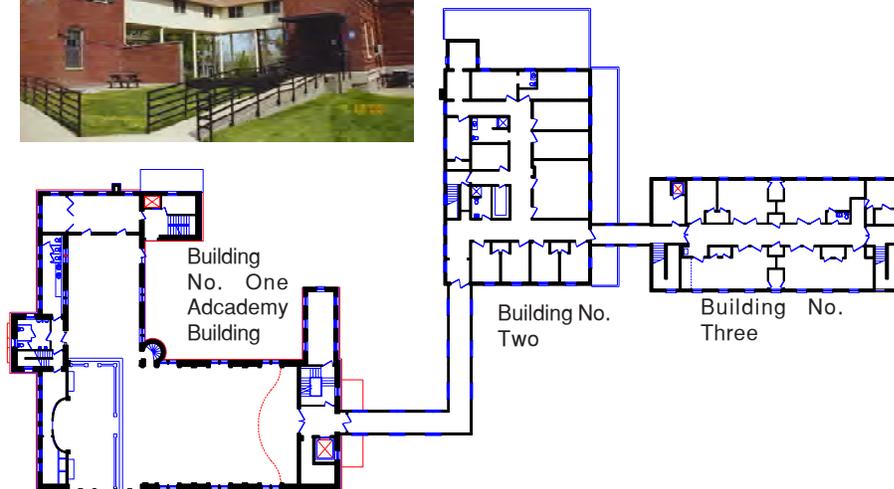

**FITZSIMONS OFFICE of
ARCHITECTURE, INC.**
112 W. Third St.
Lexington, KY 40508
859-243-0838

**FITZSIMONS OFFICE of
ARCHITECTURE, INC.**
112 W. Third St.
Lexington, KY 40508
859-243-0838


Bourbon County Fiscal Court
Donny Foley
County Judge Executive
Paris, Kentucky
Completed: Fall 2008

**FITZSIMONS OFFICE of
ARCHITECTURE, INC.**

FOA in working on the renovation of the large tower and dome structure as well as the replacement of the roof system. The tower and dome renovation will be a complete rehabilitation of the steel framed tower and sheet metal ornament. Structural repairs include the steel frame, roof structure, stone and brick masonry. The exterior parapet walls and pedimented sections of ornamental stone will be repointed. The tower drainage systems will be reworked to improve the ability to maintain the building. The interior spaces that have been damaged will be restored including the large glass dome. In addition a new mechanical and electrical system is being designed to be integrated into the existing building spaces.





Renovation of the **Bourbon County Courthouse Dome Renovation**

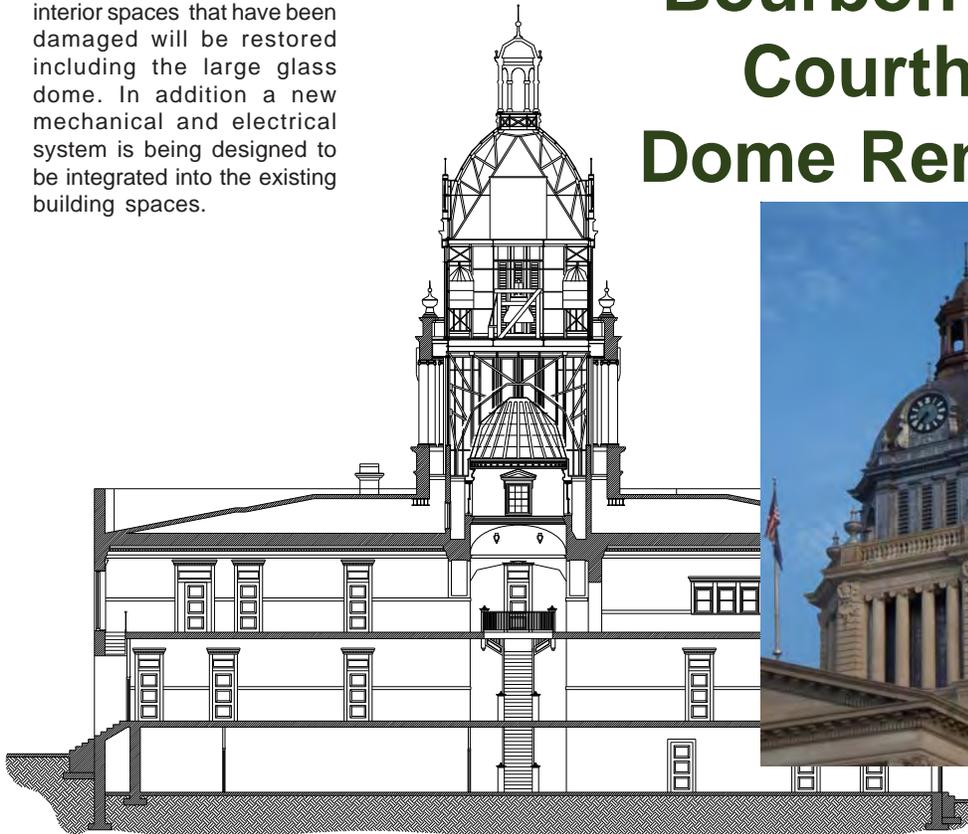


Norsworthy Auditorium Renovation GS Potts Building Renovation Lexington, Kentucky

The old Henry Clay High School, ca. 1926, is now used for the Fayette County Board of Education offices. The exterior of the building is being renovated to complete much needed work at this historic school building. Also on the site is a two story annex building which is getting an elevator. In 2001 FOA received a Historic Preservation Award for the interior restoration of Norsworthy Auditorium which is located in this building. Norsworthy Auditorium renovation and the other projects on this site, including an elevator, roof replacement, window repairs, masonry work and general exterior renovation cost two million dollars.

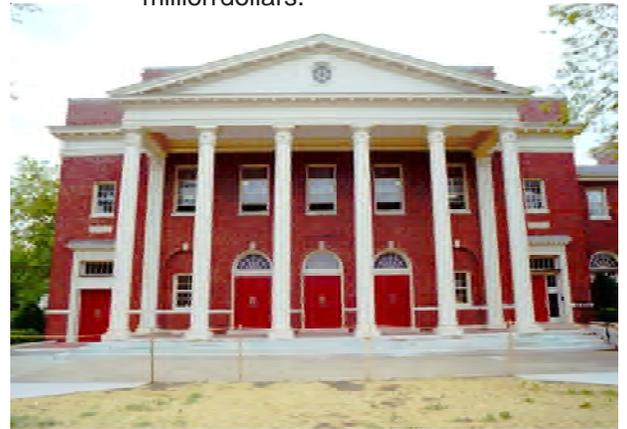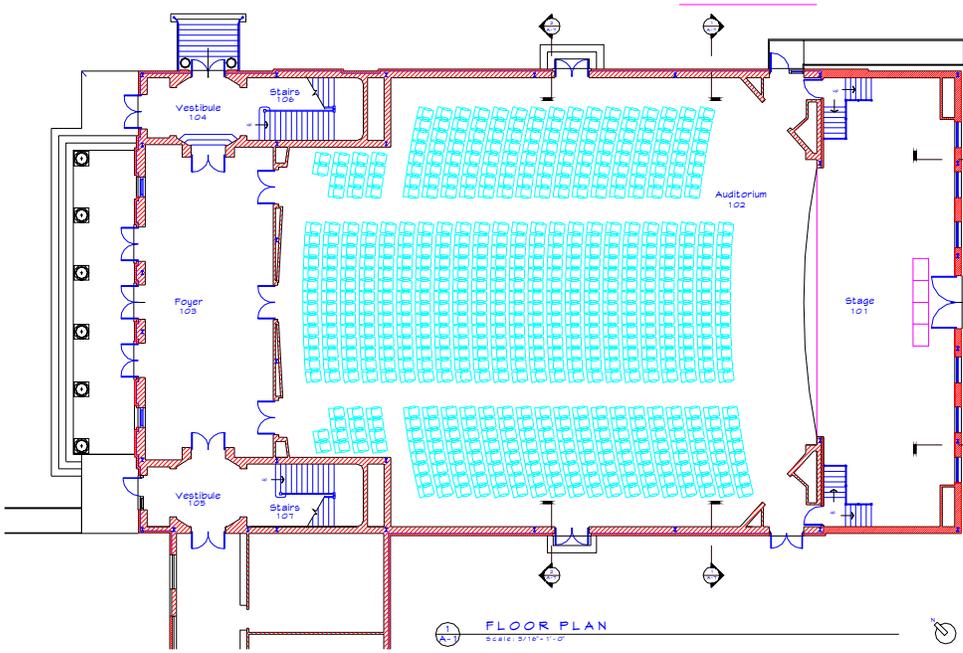


Nordsworthy Auditorium

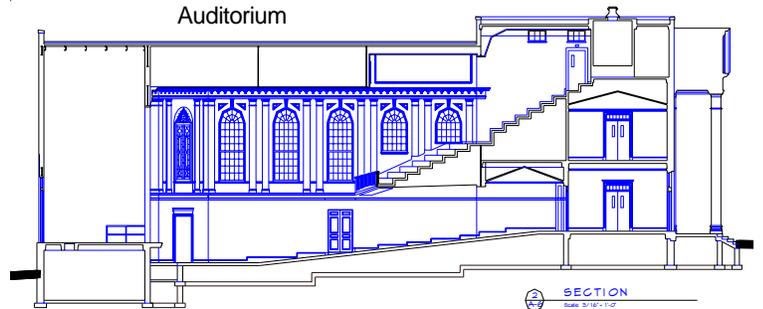

Fayette Co. Public Schools
701 W. Main Street
Lexington, KY

FITZSIMONS OFFICE of
ARCHITECTURE, INC.
112 W. Third St.
Lexington, KY 40508
859-243-0838

Guy Potts Building Renovation
(old Henry Clay High School)

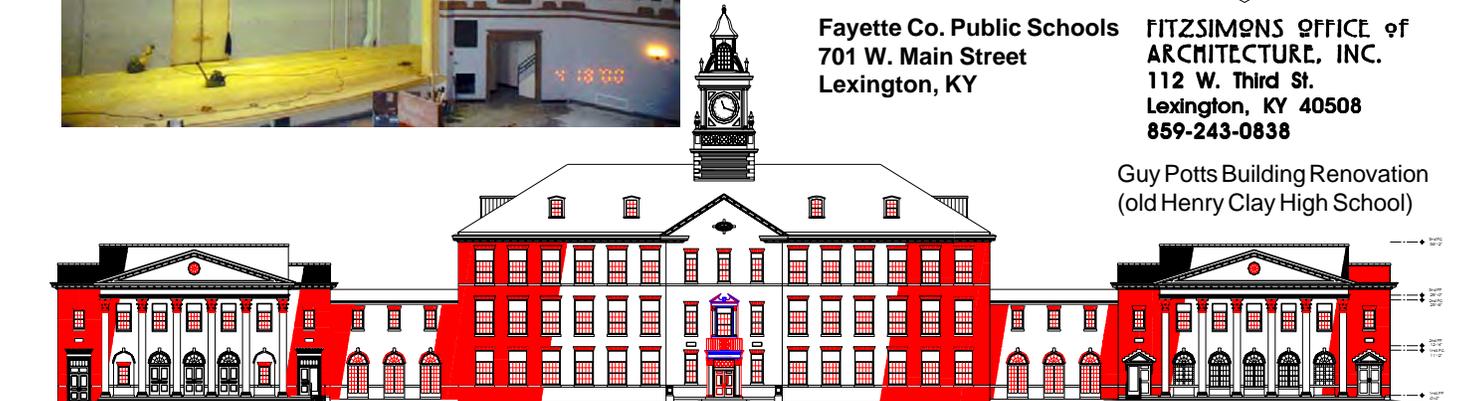


**FITZSIMONS OFFICE of
ARCHITECTURE, INC.**

**112 West Third St.
Lexington, KY 40508
859-243-0838**

The Roberts H. Williams Cultural Center is a 2-story raised basement masonry structure ca. 1892. The master plan for the full renovation and addition includes removing the existing metal fire escapes at each end of the building. With minor alterations to the floor plan and building facade, access is created to the new enclosed exit stairs to the rear. Lifesafety upgrades will include exit corridors, lighting, fire alarm, sprinklers and other modifications. Funding for Phase I has been secured and the renovation will be finished in December of 2003. The building housed Lexington's African American Orphanage until the 1980's. It is being renovated to expand the Center's program for cultural improvement.

**R.H. Williams
Cultural Center
Master Plan
Phase I Renovation
Lexington, Kentucky**

R.H. Williams Cultural Center Board
of Directors
Director
644 Georgetown Rd.
Lexington, Kentucky
859-225-5211

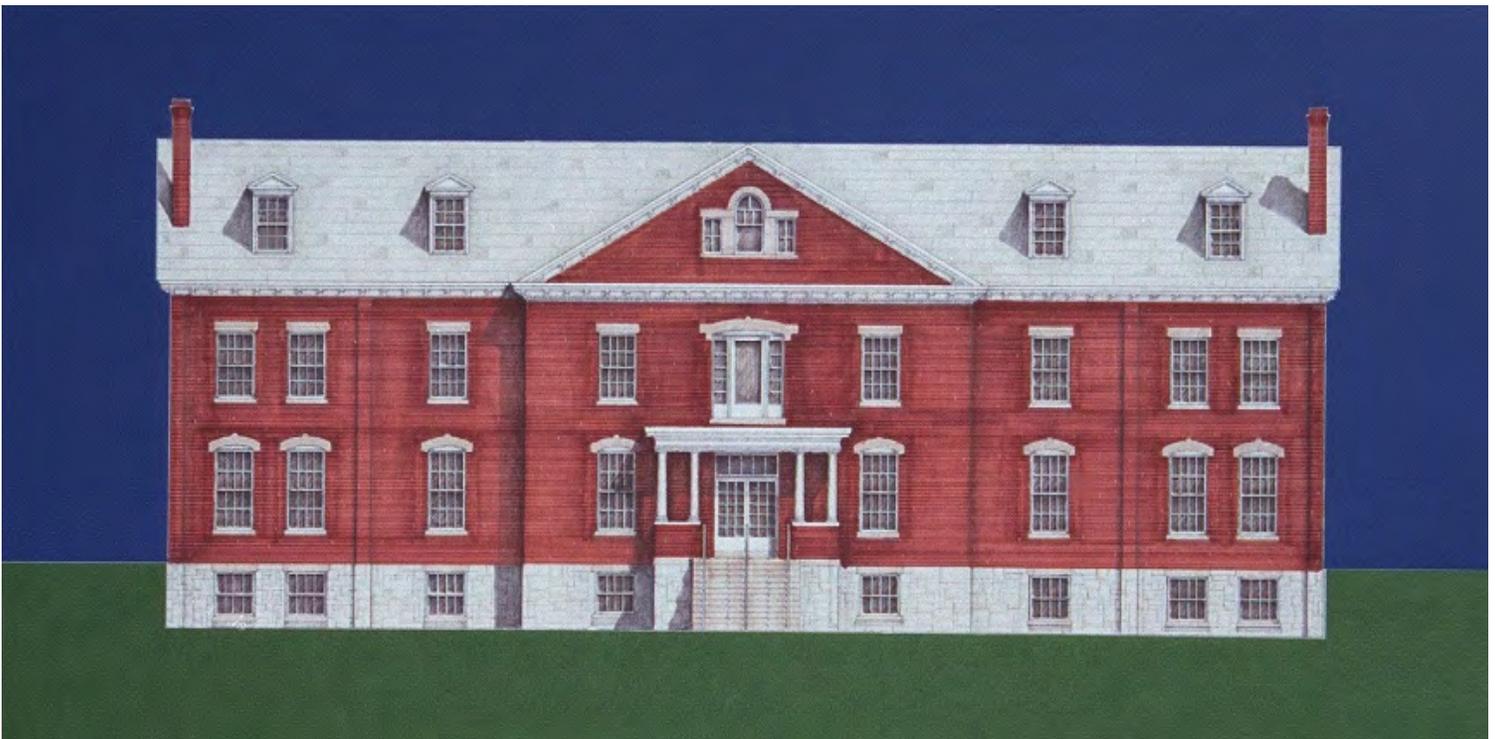




Fire Stations No. 5 and No. 6 Renovations

FITZSIMONS OFFICE of
ARCHITECTURE, INC.
112 W. Third St.
Lexington, KY 40508
859-243-0838

Fire Stations No. 5 & 6
Captain Robert King
LFUCG Division of Fire and
Emergency Services
219 East Third Street
Lexington, KY 40508
859-361-1197

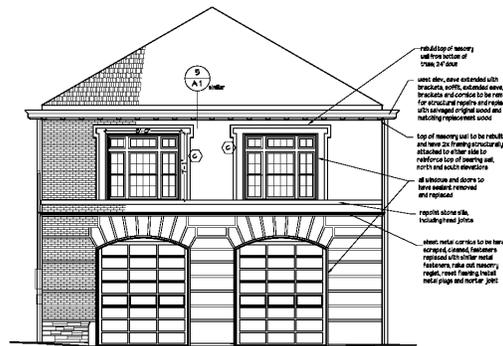


WEST ELEVATION
SCALE: 1/8" = 1'-0"



Fire Station No. 5 & 6 Renovations

Station 5 is the Maxwell Street Station. It is a historic building and all repairs were approved by historic division. The roof, gutters and windows were replaced. A new kitchen was installed and the dorm room renovated. The exterior was painted. Cost: \$145,000

Station 6 is also partially a historic building. The original section was added on to in the 1980's. This addition needed a new roof, repairs to skylight, apparatus bay entry portico, and other significant maintenance items. Cost: \$85,000



CARMAN Organization



CARMAN, formerly John L. Carman and Associates, was founded in 1980 with a philosophy of providing sensitive planning and design with an eye for the integration of technically sound responses to the natural and built environment. We have met the challenges of this philosophy with a broad range of experience with both the public and private sector. The commitment of our Landscape Architectural and Civil Engineering staff to each client has gained our firm the reputation of meeting unique demands of complex and challenging projects. Our staff listens to our clients and creates an understanding of their needs.

CARMAN has the experience and qualifications to approach an assignment in a comprehensive manner. We integrate creativity and technical expertise with an understanding of both small and large-scale environments. The integration of Landscape Architecture, Land Planning, Environmental Planning and Civil Engineering places our staff in a unique position to provide quality and timely consultation.

John Carman, President

*The Kentucky Erosion and Sediment Prevention Controls and
The United States Green Building Council
have certified and accredited three members of the CARMAN staff*

*CARMAN is Pre-Qualified by the Kentucky Transportation Cabinet, Department of Highways in
Rural and Urban Roadway Design, Construction Services and Bikeway Planning*

CARMAN employs seven licensed Landscape Architects led by Mr. John L. Carman, Senior Principal, KY license number 310. Additionally, CARMAN is permitted as an Engineering Company, permit number 1709. Civil Engineer, Mr. J. Wesley Turley, KY license number 24005, serves as the Engineer in Charge for CARMAN.

"It is not the language of painters but the language of nature which one should listen to..... The feeling for the things themselves, for reality, is more important than the feeling for pictures"

Vincent Van Gogh

CARMAN
Environments Fully Realized



The Landscape Architectural and Civil Engineering staff at CARMAN provides comprehensive site design, land planning, and site/civil engineering services to a broad spectrum of clientele. Our staff consists of the following personnel by specialized discipline:

Landscape Architects, Registered	7
Landscape Architect, Intern	3
Civil Engineer	1
Administrative Professionals	2

CARMAN's main office is located in Lexington, Kentucky with a satellite office located in Louisville, Kentucky. These two locations allow CARMAN to serve a broader geographical area without compromise to the time and attention we provide to our valuable clientele. CARMAN has provided professional services since 1980.

The CARMAN staff of Landscape Architectural and Civil Engineering professionals take pride in creating and integrating the natural and built environments for people and the protection of the natural, indigenous resources of those environments. The CARMAN office has a long history of creating award-winning Sustainable environments used for a variety of purposes such as Education, Recreation and Placemaking in the Public Realm.

Professional Services Provided by CARMAN

The staff at CARMAN prides themselves in integrating a full range of site design services into their daily practice of improving the quality of both the natural and built environment. From the creation of a natural wildlife habitat to the development of a planned commercial center, the experienced staff of Landscape Architects at CARMAN provides sensitive solutions to specific site conditions and user needs. Uses of the landscape including Recreational, Institutional, Industrial, Housing, Educational, and Municipal facilities are adapted and created by our staff within the context of their site without compromising efficient, economical design. Our firm provides quality consulting services to Federal, State, and Local Governments; private developers; school boards; and architects in an integrated team method to gain maximum results.

Strategies and directions for long-range comprehensive planning of an environment are fundamental to the success of the development of both large and small-scale environments. Our staff provides award-winning management and master plans for a variety of projects that are anticipated to be long-term in their development process. The foresight and perception of site development needs of a community, region, or specific environment are integrated into a planned scheme that is mapped into priorities, phases, and logical approaches for the best outcome. Large-scale industrial developments, university/college campuses, State Parks, and planned unit developments are all land uses that have been planned for long-range development by CARMAN. The ability to demonstrate specific impacts to long-range planning by performing Environmental Assessments, Scenic and Visual Assessments, Economic Feasibility, and Action Planning are all associated land planning functions offered by CARMAN.

As a comprehensive site design consultant, CARMAN offers Civil Engineering as a means to provide quality, functional design solutions. The Civil Engineering staff recognizes the need to engage technical workability into each and every design solution and strives to integrate pragmatic engineering needs of infrastructure, stormwater management, and utilities without compromising quality design and insuring technically efficient results. CARMAN has provided Civil Engineering services since 1992 as an added value to comprehensive site design services.

Landscape Architecture



Land and Urban Planning



Civil Engineering



Federal I.D. #61-1033777

John L. Carman, FASLA, RLA
Sr. Partner/Principal



John L. Carman established the firm of CARMAN in 1980 after successful practice with companies providing service in Landscape Architecture, Engineering, and Construction Management in Lexington, Kentucky and Huntington, West Virginia. With this training to build upon, Mr. Carman has since established an award-winning firm that provides services to a wide variety of clientele. Mr. Carman prides himself in being a “hands-on” manager and is always very active in each phase of all projects.

John Carman’s experience extending over a 35-year period has been with large and small-scale projects ranging from Educational Facility Planning, Community Planning and Design, Site Engineering, Athletic Facility Design, and Environmental Planning. Mr. Carman is acknowledged as being on the cutting edge with creative and technically superior site design, particularly in the areas of storm water management and supporting site improvements. Mr. Carman contributes routinely at the University of Kentucky Landscape Architecture Department as adjunct professor and guest lecturer in a variety of design, construction, and professional practice courses.

Mr. Carman has developed a Landscape Architectural, Urban Design and Civil Engineering practice that has extended over a broad spectrum of public and private areas of design and planning. His practice has extended to Louisville where an office was established in 2007.

Mr. Carman recently presented project case studies on Complete Streets at the Regional Transportation Summit.

RELEVANT PROJECT EXPERIENCES

Louden House
Lexington, Kentucky

Cardome Community Center
Georgetown, Kentucky

Carnegie Center
Lexington, Kentucky

Kimball House
Lexington, Kentucky

Lyric Theater and Museum
Lexington, Kentucky

Solomon Family and Community Center
Ft. Jackson, South Carolina

EDUCATION

B.S. Landscape Architecture
University of Kentucky, 1976

PROFESSIONAL REGISTRATION

Landscape Architect, states of:
Kentucky - #310
CLARB - #797

PROFESSIONAL AFFILIATIONS

American Society of Landscape
Architects Member, Fellow

Council of Landscape Architectural
Registration Boards - National Board of
Directors, Past President

Kentucky Landscape Architectural Reg-
istration Board - Appointed 1989, 1994,
2006

KYDOT Paris Pike Design Review Task
Force

University of Kentucky Life Time Alumnus
and Fellow

‘The Masters’ PGA Golf Tournament Mar-
shal - Augusta National

CONTINUING EDUCATION

Engineering Methods for Improving
Watershed Quality

Incorporating Bioengineering Techniques
in Erosion and Sediment Control

Biotechnical Erosion Control Techniques:
Matching Techniques to Sites

Urban Stormwater Management

DPIC Contract Review and Revision

Urban Stormwater Management and De-
tention Pond Design

Ecological Restoration

Harvard Graduate School of Design -
Golf Course Design Course

Chris Howard, RLA, LEED AP
Principal / Partner



Chris Howard has been associated with CARMAN since 1996. Prior to 1996, Mr. Howard worked in a Whitesburg, Kentucky architectural office providing site design for a wide variety of projects in eastern Kentucky. As a project manager for CARMAN, Mr. Howard has actively managed many municipal, educational, recreational, industrial, and commercial facility projects. His responsibilities include master planning, site design, construction drawings, and construction administration.

As part of Chris's professional interest he has become a LEED accredited professional and applies green design principles to the CARMAN projects in a variety of creative means. Chris' experience in sustainable design has allowed him to engage these principles in many project types, particularly in the educational sector. His environmental sensitivity and awareness on school sites and campuses has provided many benefits with K -12, college and university unique environments.

RELEVANT EXPERIENCE

MSU Welcome and Alumni Center
Morehead, Kentucky

Living Arts and Science Center
Lexington, Kentucky

Lyric Theater and Museum
Lexington, Kentucky

Big Ass Fans Research and Manufacturing Complex
Lexington, Kentucky

New Fayette County High School
Lexington, Kentucky

East Market Street – NuLu Corridor Improvements
Louisville, Kentucky

AWARDS

American Society of Landscape Architects, Kentucky Chapter
Design Honor Award for Big Bone Lick State Park, Discovery Trail - Union, Kentucky,
2000

EDUCATION

B. S. Landscape Architecture
University of Kentucky, 1992

PROFESSIONAL REGISTRATION

Landscape Architect, state of:
Kentucky - #528

LEED®AP Professional

Certified Kentucky Erosion Prevention
and Sediment Control Program

PROFESSIONAL AFFILIATIONS

Council of Landscape Architectural
Registration Boards (CLARB) - Landscape
Architecture Registration Exam (LARE)
Grader

University of Kentucky, Department of
Landscape Architecture - Adjunct Profes-
sor, 2000

CONTINUING EDUCATION

Stormwater Pollution Prevention Plan
Preparer's Course 2010

LEED - NC Technical Review Training,
2005

Stormwater Design Seminar, 2003

National Recreation and Park Association
(NRPA) Southern Regional Conference,
"Regional Greenway Planning", 2002

Land Development Provisions to Protect
Water Quality, 2001

Rails to Trails and Greenways
Conference, 2000

John Wesley Turley, PE
Civil Engineer - Associate



Mr. Wes Turley is involved in all phases of the company operations. His responsibilities range from civil engineering, construction administration, land development, utilities, sanitary sewer, water, industrial engineering and management.

With over twelve years of experience, Mr. Turley has worked in the Civil Engineering industry with a variety of experience including stormwater design, sanitary sewer, water distribution, retention basin, and roadway design. He has also completed stormwater and utility designs for commercial projects, institutional developments and right-of-way improvements for community development projects.

As the principal engineering associate for CARMAN, Mr. Turley is fully involved in all aspects of engineering design and management for most all CARMAN projects. This responsibility includes permitting with local, State and Federal agencies in addition to responsibilities of projects during construction.

RELEVANT EXPERIENCE

- 4th State Veterans Affairs Nursing Home**
Radcliff, Kentucky
- Magoffin County High School**
Salyersville, Kentucky
- New Fayette County High School**
Lexington, Kentucky
- East Market Street – NuLu Corridor Improvements**
Louisville, Kentucky
- Squires Elementary School**
Louisville, Kentucky
- Fairview Independent High School**
Fairview, Kentucky

EDUCATION

B.S. Civil Engineering
University of Kentucky, 1999

PROFESSIONAL REGISTRATION

Kentucky, Ohio, Indiana, Tennessee
Arizona

Certified Professional - Erosion and
Sediment Control

PROFESSIONAL AFFILIATIONS

Kentucky Society of Professional
Engineers

National Society of Professional
Engineers

American Society of Civil Engineers

PROFESSIONAL DEVELOPMENT

2010 KSPE Leadership Graduate
ICC Special Inspections Training; 2010

Critical Path Method: Intro to the Method
and Software

CPESC (Erosion and Sediment Control
Course); 2009

Channel Impacts/Bedload Sediment
Natural Channel Design--Conception to
Construction

Engineering Green Infrastructure

Louisville MSD Wet Weather Program

SD1-Consent Decree Update

Lexington Wastewater and Stormwater
Programs

Green Infrastructure & Wet Weather
Management

Pump Stations going silent, Ecosystem
Approach to Green

Introduction to HEC-RAS Culvert
Hydraulics

KY/TN ICSC Idea Exchange

CARDOME CENTER MASTER PLAN

Georgetown, Kentucky


CLIENT: City of Georgetown
Ms. Sherry Williams, Director
502.863.1575



CARMAN was commissioned by the City of Georgetown to develop a master plan for this beautiful, historic property acquired in 1987 as a community center.

A campus of 10 buildings set on 87 acres dates back to 1890 when the Sisters of Visitation acquired the property and constructed the Cardome Visitation Academy.

Bordered by the Elkhorn Creek and U.S. 25, the property is just to the north of downtown Georgetown. The rolling, bluegrass terrain accented by large, hardwood trees was owned through the late 18th and 19th centuries by some of Kentucky's most prominent families. From Colonel John Floyd in 1774 to James F. Robinson, Kentucky's governor in 1862, the preservation of the historic record of this site is paramount to its future use.

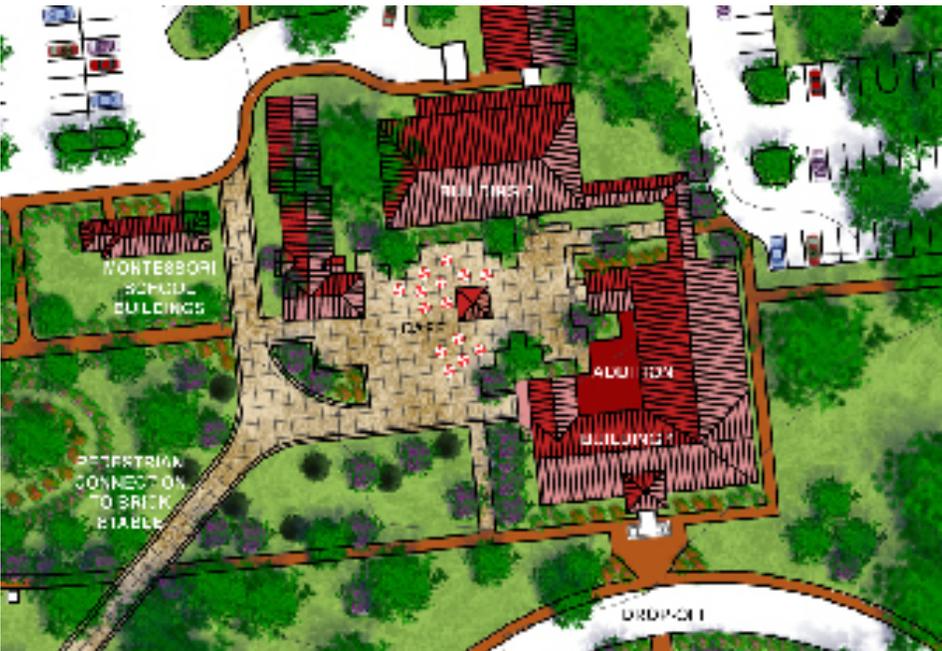

The master plan included a trail system for passive recreational opportunities along with siting of new community buildings, parking areas, and an outdoor classroom pavilion. This pavilion is designed to be an educational center along the trail system while affording views into the surrounding landscape.



CARNEGIE LITERACY CENTER
Lexington, Kentucky

CLIENT: Lexington-Fayette Urban County Government
200 East Main Street
Lexington, Kentucky 40507



When the Lexington Public Library expanded and relocated to another facility, the original library building located in Lexington's historic Gratz Park was vacated.

The historic building was too valuable not to utilize for other purposes, and it was determined that the building was to be used as a community learning center.

The building and site required considerable modifications to meet code requirements for accessibility and to accommodate the new user needs.

CARMAN was commissioned to provide plans for site accessibility modifications, parking lot expansion, and landscape enhancements.

All plans were reviewed by the Historic Architectural Review Board for strict compliance to local preservation standards and compliance with historically correct features of the site and building.



LOUDEN HOUSE
Lexington, Kentucky

CLIENT: Lexington-Fayette County Government
200 East Main Street
Lexington, Kentucky 40507



CARMAN was selected by Fitsimons Architecture to provide site planning, landscape architecture and civil engineering services for the renovation of the Historic Louden House.

CARMAN provided renovation and site enhancements for the historic structure that is utilized for studio and gallery space for the Lexington Art League.

Designated Contact & Principal-in-Charge

Whitley Casey PE, Principal
859-277-8177
whitley.casey@stweng.com

Principals-In-Charge

The accessible involvement of our principals results in continuity and a solution-oriented approach to projects.

Whitley Casey, PE, Principal
Electrical Engineer Registration # 25711
whitley.casey@stweng.com

Firm Information & Background

Since 1981, ShROUT Tate Wilson Engineers has been providing superior consulting engineering services for mechanical, electrical, plumbing and fire protection systems. In March of 2014, ShROUT Tate Wilson Engineers and KTA, Inc. announced a merger of the firms. Together, we boast over half a century of experience designing systems that are sustainable by both the operator and the environment.

We are the authority in high-efficiency Geothermal and Variable Refrigerant Volume (VRV) design as well as classical chilled water, hot water, and steam systems. When this expertise is coupled with our ongoing drive for learning, we deliver innovative HVAC designs. Our electrical design expertise includes energy efficient lighting, power distribution systems, and low voltage communication systems.

It may sound trite, but to us, our personality is a big piece of why we are your partner beyond the first-project honeymoon. The rest of the pie is made up of early & often communications and a "roll-up our sleeve" attitude.

Your projects are our business. This is why we don't shy away from problems when they occur. Instead, we apply stick-to-itiveness and professionalism to address challenges like schedule and coordination.

In-House Personnel

The next big challenges are here. Not just in new advances, but also making better use of our buildings and the resources we have. Like you, we are thought leaders, leading the way with progressive work and green building projects in and for our community.

We continue to expand our firm's talent pool, making us stronger than ever. We now have a total of 29 dedicated professionals on staff.

- Professional Engineers (PE) - 10
- LEED Accredited Professionals (LEED AP) - 9
- Certified Commissioning Authorities (CxA) - 5
- Certified Energy Managers (CEM) - 3
- Registered Communications Distribution Designer (RCDD) - 1

References

Bill Wallace

Director, Facility Design & Construction
Fayette County Public Schools
859-381-3824
bill.wallace@fayette.kyschools.us

Bill Slone

Associate Director of M/E Engineering
Branch
Division of Engineering & Contract
Administration
Commonwealth of Kentucky
403 Wapping Street
Frankfort, KY 40601
(502) 782-0333
bill.slone@ky.gov

Tom Calkins

Finance Director
City of Nicholasville
(859) 885-9473
tom.calkins@nicholasville.org

CARVER COMMUNITY CENTER RENOVATIONS

Owner:

Lexington-Fayette & Urban County
Government

Contact:

Joyce Thomas
859-258-3054

Project Location:

Lexington Kentucky

Project Cost:

\$1,300,000 (HVAC)
\$2,000,000 (Restroom)

Project Size (Building):

26,050 Square Feet

Status:

Completed 2012 (HVAC)
Completed 2015 (Restroom)



The **Carver Community Center** once served as an elementary school in downtown Lexington from 1934 until the 1970's. Currently, the building supports various community activities and classes.

In 2012, our firm began work on a renovation that included a full HVAC replacement, roof repair, and electrical upgrades. The HVAC system included a Variable Refrigerant Volume (VRV) System with cassette units throughout the building. A separate air-cooled rooftop unit was designed to serve the gymnasium area and a rooftop energy recovery unit was included for the required outside air needed in the building. A new DDC control system was also installed. Electrical upgrades were included to accommodate the new HVAC system.

In 2014, STW was selected to design the first floor restroom renovation and replacement of adjacent drinking fountains. The restroom layouts on the first floor were rearranged and all new plumbing fixtures and piping were included to accommodate the new design. New light fixtures and hand dryers were included. The new drinking fountain includes a bottle filler station.

CAMPTON SCHOOL APARTMENTS & COMMUNITY CENTER

Owner:

AU Associates
Lexington, Kentucky

Contact:

Holly Wiedemann
859-233-2009

Project Location:

Campton, Kentucky

Project Cost:

\$2,500,000 (\$72.41 cost per sf)

Project Size (Building):

29,869 Square Feet

Status:

Completed 2015



The **Campton School Apartments** is a adaptive reuse of the historic Old Wolfe County High School into 19 units of mixed-use, low-income elderly housing and the new **Wolfe County Community Center**. Of particular importance to this project was the preservation of the building's historic character. This building is listed on the National Register of Historic Places.

The residential interior is completely modernized with new HVAC, plumbing and electrical systems featuring new energy efficient appliances. The Community Center also includes brand new mechanical, electrical, and plumbing systems and includes public restrooms, a concession area, a new stage and associated sound and lighting systems and a fitness center.

DOCUMENT: RESUME

WHITLEY C. CASEY, P.E., *Principal*



Education

Bachelor of Science in Electrical Engineering, Minor in Mathematics, Graduated Magna Cum Laude, May 2003
University of Kentucky College of Engineering

Relevant Project Experience

- LFUCG Fire Station #2
- LFUCG Dixie Pump Station
- Lexington Public Library Palumbo Renovation
- Forkland Community Center Renovation
- Carver Community Center – HVAC Replacement
- Bourbon County Library
- St. Peter Claver Catholic Church
- University of Kentucky Men's Basketball Team Locker Rooms, Rupp Arena
- Administrative Office of the Courts Office Renovation
- Asbury University Electrical Study
- Campton School Apartments

Professional Experience

Shrout Tate Wilson Consulting Engineers, Lexington, KY

2003 - Present

Mr. Casey leads STW's team for the firm's most challenging projects. His responsibilities also include the design of lighting, power distribution, emergency power systems, fire alarm, sound/intercom, telephone/data and miscellaneous control systems for our Municipal, Education, Commercial, Church, and Wastewater Treatment Plant projects. Whitley incorporates systems into contract documents using AutoCad and Revit MEP. He also models and simulates building performances using EQuest software to verify designs meet Energy Star requirements.

Primary Areas of Experience

- Lighting Design
- Energy Conservation
- Fire Alarm Systems
- Communication Systems
- Power and Distribution
- Special Systems
- Computer Network Systems
- Theatrical Systems
- Professional Sound Systems

Registrations

- PE (Professional Engineer) KY Registration # 21482
- LEED (Leadership in Energy and Environmental Design) Accredited Professional
- CEM (Certified Energy Manager)
- CxA (Certified Commissioning Authority)
- L.S.I.T. (Land Surveyor in Training)

Professional Affiliations

- US Green Building Council Member
- Kentucky Society of Professional Engineers
- National Society of Professional Engineers
- Association of Energy Engineers

Community Involvement

- One to One Reading Program at William Wells Brown Elementary

LEXINGTON 628 Winchester Road
Lexington, KY 40505
(859) 277-8177

LOUISVILLE 207 West Market Street, Suite 300
Louisville, KY 40202
(502) 829-3001

CORY V. SHARRARD, P.E., *Project Manager, Mechanical Engineer*



Professional Experience

Shrout Tate Wilson Consulting Engineers, Lexington, KY

2014-Present

Responsible for the design, specification, estimation and construction administration of plumbing, fire suppression, and mechanical projects at Shrout Tate Wilson. Designs include: VAV Air Handling Unit systems, Central Chilled Water and Central Boiler systems, Central Geothermal systems, Central Geothermal Modular Heat pumps with Variable Primary Flow, Energy Recovery systems, Hybrid Geothermal systems, and Solar Hot Water Heating systems, Air-cooled VRV systems, and Water-cooled VRV with Hybrid Geothermal systems.

KTA, Inc., Consulting Engineers, Lexington, KY

1998-2014

KTA Principal. Responsible for mechanical cost estimating, cost tracking, and plan submittal for the majority of projects at KTA, Inc. Also responsible for calculating comparative life cycle cost analyses to prepare studies for various projects. Projects included educational, commercial, government, and healthcare.

Primary Areas of Experience

- HVAC
- Plumbing
- Fire Protection
- Central Plants
- Geothermal
- Chilled Beam
- Energy Recovery
- Temperature Controls

Education

Bachelor of Science in Industrial Technology, May 1996
Murray State University

Bachelor of Science in Mechanical Engineering, May 1998
University of Kentucky

Related Experience

- Carver Community Center – Restroom Renovation Phase 1
- Carver Community Center – HVAC Replacement
- Lyric Theatre – Addition/ Renovation
- Loudon House Renovation
- UK Arboretum New Restroom Building
- Pleasant View House Renovation
- Eastern Kentucky University Housing Study
- Scott Schools Facility Surveys
- Fayette County Public Schools Facility Survey and Assessment for future Preschool Building
- Turner Elementary Feasibility Study
- Stonewall Elementary School Renovation and Addition

Registrations

- PE (Professional Engineer) KY Registration # 23106
- LEED (Leadership in Energy and Environmental Design) Accredited Professional
- CxA (Certified Commissioning Authority)

Professional Affiliations

- Society of Marketing Professional Services, Membership Chair, Past President
- Kentucky Society of Professional Engineers, Professional Development Committee Vice Chair
- American Society of Heating, Refrigerating and Air Conditioning Engineers (ASHRAE), Secretary

DOCUMENT: RESUME

JIM SMITH, *Electrical Designer*



Professional Experience

Shrout Tate Wilson Consulting Engineers, Lexington, KY

2014 - Present

Jim brings an unmatched attention to detail to his projects. For STW, Jim works on a variety of building types including multi-unit housing, historic renovations, healthcare, and K-12. Mr. Smith is responsible for the design and specification of electrical systems including: energy efficient lighting and power distribution systems, emergency power systems, communication systems, and fire alarm systems.

Parsons Electric, Inc., Lexington, KY

2000-2014

Design of building electrical systems for all phases of development. Incorporated power, lighting and systems (including communications, fire alarm, paging, security, card access, closed-circuit television, nurse call, code blue, and grounding) to building design. Project experience ranged from small renovations to projects over one million square feet. Jim also provided BIM coordination using Autodesk Revit.

Certifications

- Kentucky Master Electrician License
- FCC Class 3 Commercial Radiotelephone Operator's Permit
- Microsoft Certified Systems Administrator
- Information Technology A+
- Information Technology Fundamentals

Primary Areas of Expertise

- Lighting Design
- Energy Conservation
- Fire Alarm Systems
- Communication Systems
- Power and Distribution
- Special Systems
- Computer Network Systems
- Theatrical Systems
- Professional Sound Systems

Education

**Associate in Applied Science,
Business Administration, 2014**

**Associate in Applied Science,
Computer & Information
Technology, 2012**

**Associate in Science, General
Studies, 2012**

**Associate in Arts, General
Studies, 2012**

Kentucky Community & Technical
College System

Relevant Project Experience

- Lexington Fire Department
Maintenance Ph 2 Building
- Bluegrass Station Building 3
Bay A
- Marriott Town Place
- Maxwell Elementary HVAC
Renovation
- Parkway Plaza Apartment
Renovation
- State Office Building
Renovation
- Lexington Catholic High School
Facility Surveys
- Boone County HVAC
Renovation Phase 2

LEXINGTON 628 Winchester Road
Lexington, KY 40505
(859) 277-8177

LOUISVILLE 207 West Market Street, Suite 300
Louisville, KY 40202
(502) 829-3001

EQUAL OPPORTUNITY AGREEMENT

The Law

- Title VII of the Civil Rights Act of 1964 (amended 1972) states that it is unlawful for an employer to discriminate in employment because of race, color, religion, sex, age (40-70 years) or national origin.
- Executive Order No. 11246 on Nondiscrimination under Federal contract prohibits employment discrimination by contractor and sub-contractor doing business with the Federal Government or recipients of Federal funds. This order was later amended by Executive Order No. 11375 to prohibit discrimination on the basis of sex.
- Section 503 of the Rehabilitation Act of 1973 states:

The Contractor will not discriminate against any employee or applicant for employment because of physical or mental handicap.

- Section 2012 of the Vietnam Era Veterans Readjustment Act of 1973 requires Affirmative Action on behalf of disabled veterans and veterans of the Vietnam Era by contractors having Federal contracts.
- Section 206(A) of Executive Order 12086, Consolidation of Contract Compliance Functions for Equal Employment Opportunity, states:

The Secretary of Labor may investigate the employment practices of any Government contractor or sub-contractor to determine whether or not the contractual provisions specified in Section 202 of this order have been violated.

The Lexington-Fayette Urban County Government practices Equal Opportunity in recruiting, hiring and promoting. It is the Government's intent to affirmatively provide employment opportunities for those individuals who have previously not been allowed to enter into the mainstream of society. Because of its importance to the local Government, this policy carries the full endorsement of the Mayor, Commissioners, Directors and all supervisory personnel. In following this commitment to Equal Employment Opportunity and because the Government is the benefactor of the Federal funds, it is both against the Urban County Government policy and illegal for the Government to let contracts to companies which knowingly or unknowingly practice discrimination in their employment practices. Violation of the above mentioned ordinances may cause a contract to be canceled and the contractors may be declared ineligible for future consideration.

Please sign this statement in the appropriate space acknowledging that you have read and understand the provisions contained herein. Return this document as part of your application packet.

Bidders

I/We agree to comply with the Civil Rights Laws listed above that govern employment rights of minorities, women, Vietnam veterans, handicapped and aged persons.

Signature

Shrout Tak Wilson
Name of Business

WORKFORCE ANALYSIS FORM

Name of Organization: Shrout Tate Wilson Consulting Engineers

Date: 12 / 8 / 2015

Categories	Total	White		Latino		Black		Other		Total	
		M	F	M	F	M	F	M	F	M	F
Administrators	1		1								
Professionals	10	9	1								
Superintendents											
Supervisors											
Foremen											
Technicians	5	4	1								
Protective Service											
Para-Professionals	9	7	2								
Office/Clerical	4		4								
Skilled Craft											
Service/Maintenance											
Total:	29	20	9								

Prepared by: Whitley Casey, Principal
Name & Title



PYRAMID CONSULTING STRUCTURAL/CIVIL ENGINEERS, INC.

432 SOUTH BROADWAY LEXINGTON, KENTUCKY 40508 (859) 252-1678 / FAX (859) 226-0512

pyramidcse@qx.net

EXECUTIVE SUMMARY

FIRM DESCRIPTION

Pyramid Consulting Structural/Civil Engineers, Inc. was founded in 1994 by Mohammad R. Seraji, its current president.

Pyramid Consulting Structural/Civil Engineers, Inc. is a full service structural consulting firm offering extensive experience in the structural design development of emergency facilities, commercial/industrial buildings, schools, churches, hospitals, incarceration facilities, airport facilities, and highway transportation superstructures/substructures, structural analysis and design including dynamic/vibration analysis, foundations, software development, and forensic engineering. We have project managers on staff with experience in the design-build environment where quick turnaround is critical.

Our office is located at: 432 South Broadway, Lexington, KY 40508

Contact Person: Mohammad R. Seraji, P.E., President
Phone: 859-252-1678
Fax: 859-226-0152
E-Mail: mo.pyramid@qx.net

PROJECT TEAM

PRINCIPLE-IN-CHARGE – Mohammad R. Seraji P.E.
PROJECT MANAGER – Jordan M. Yeiser P.E.
PROJECT ENGINEER – Dave Mills, E.I.T.
CAD TECHNICIAN – Standley Shelton

Please see attached resumes for more information about the project team's relevant experience.



PYRAMID CONSULTING STRUCTURAL/CIVIL ENGINEERS, INC.

432 SOUTH BROADWAY LEXINGTON, KENTUCKY 40508 (859) 252-1678 / FAX (859) 226-0512

pyramidcse@qx.net

MOHAMMAD R. SERAJI, P.E.

Structural/Civil Engineer

President

EXPERIENCE

For the past seven years, Mr. Seraji has been a volunteer with the Post Disaster Search and Rescue Operations. He has assisted in post-disaster efforts, most recently during the West Liberty tornados. Mr. Seraji also volunteers to teach courses preparing various rescue centers on how to evaluate and temporarily shore damaged buildings following a catastrophic event.

President, Pyramid Consulting Structural Engineers, Inc., Lexington, Kentucky -- Principal in charge of Lexington office. Responsible for management of five full-time and two part-time employees. Design development of structural plans and specifications, structural site monitoring, shop drawing review.

Project Engineer/Structural Engineer, Buell-Fryer & Associates, Lexington, Kentucky -- Responsible for preparing structural plans and directing the design and drafting department. Drafted and edited structural specifications, coordinated work with clients and other design team consultants, performed site monitoring and checking shop drawings of construction in progress.

Structural Engineer/Detailer, Southeast Steel, Lexington, Kentucky -- Performed structural engineering design and supervised drafting department, managing and coordinating all projects.

Lecturer, University of Louisville Speed Scientific School, Louisville, Kentucky -- Responsible for instructing courses in graphics, surveying, strength of material lab and statics, and strengths of material.

EDUCATION

University of Louisville, Master of Engineering (pending)

University of Kentucky, B.S.C.E., 1982

PROFESSIONAL MEMBERSHIPS


Structural Engineers Association of Kentucky.

Consulting Engineers Council of Kentucky.

REGISTRATION

Professional Engineer in Kentucky, Alabama, Arizona, Arkansas, Colorado, Connecticut, Delaware, Florida, Idaho, Indiana, Iowa, Kansas, Louisiana, Maryland, Michigan, Minnesota, Mississippi, Missouri, Montana, Nebraska, New Jersey, New Mexico, New York, North Carolina, North Dakota, Ohio, Oklahoma, Pennsylvania, South Carolina, South Dakota, Tennessee, Texas, Vermont, West Virginia, Wisconsin, & Wyoming.

Kentucky P.E. License #: 17387



PYRAMID CONSULTING STRUCTURAL/CIVIL ENGINEERS, INC.

432 SOUTH BROADWAY LEXINGTON, KENTUCKY 40578 (859) 252-1678 FAX (859) 226-0512

pyramidcse@qx.net

Historical Preservation and Renovation Projects:

Fulton County Courthouse

Fulton County, Kentucky
Client: Fulton County Fiscal Court
Construction Cost: \$3,200,000
Completion Date: 1994

The scope of services for this project included renovation and addition of a late 1800's courthouse to comply with A.O.C. standards and handicapped accessibility to all floors. The structural design consisted of seismic retrofitting of the structure for zone 3, an addition of an elevator shaft for access to all floors, supporting and renovating the existing attic for record storage, and preservation of the existing exterior masonry walls.

Best Lovell Building

Richmond, Kentucky
Client: The City of Richmond, Kentucky
Construction Cost: \$2,200,000
Completion Date: 1997

The scope of services for this project included the renovation of a 1901 three story multi-wythe brick building. This building was used for the City of Richmond government office use. The structural design consists of removing and replacing the existing fire damaged floor with a new framing system, addition of an elevator to access all floors, and deepening the existing basement in order to provide additional headroom for accessibility to the elevator machine room, and mechanical and electrical rooms. Our scope of work also included preservation and reinforcement of exterior masonry walls.

Bourbon County Courthouse

Paris, Kentucky
Client: Bourbon County Fiscal Court
Construction Cost: \$2,200,000
Completion Date: 1998

This project was a renovation of a 1903 - three story courthouse. The structural design consisted of an elevator addition to access all floors, restoration and reinforcement of long span sand stone steps, reinforcement of a clock tower and demolition and restructuring of an existing exterior elevated front entry.

Arabat Cultural Center

Moscow, Russia

Client: Ellerbe Beckett

Construction Cost: \$350,000,000

Completion Date: 1997

Pyramid Consulting Structural/Civil Engineers, Inc.'s scope of service was to review the report prepared by the Structure Protection Research and Engineering Center and to assist Ellerbe Beckett in calculating the dynamic properties of the structure and recommend an appropriate type of vibration isolation in order to reduce vibration transmission to the super structure due to moving of the underground subway line.

1840 First Presbyterian Church Tower

Frankfort, Kentucky

Client: The First Presbyterian Church, Mr. Gleason Wheatley

Construction Cost: \$460,000

Completion Date: 1999

The First Presbyterian Church was originally built in 1815. The building had been exposed to water which has caused extensive damages to members such as main piers, arches and other structural compounds. The water damage has caused the weakening of the pier which resulted in main piers twisting and pulling away from their original location which in turn has caused distress and failure of other wall components such as archways and building buttresses. In order to renovate the existing structure a full evaluation of the structure was undertaken after a failed attempt by a different project team. Pyramid Consulting Structural/Civil Engineers, Inc. was retained to provide structural services. The structural work involved stabilization and reconstruction/reinforcing of an 85 foot tall masonry load bearing tower with 4 main piers and other load bearing structural wall components.

Madison County Courthouse

Richmond, Kentucky

Client: The City of Richmond, Kentucky

Construction Cost: \$3,200,000

Completion Date: 1998

This project scope of services involved the renovation of a late 1800's federal district courthouse and three-story addition. The renovation consisted of removal of a number of main multi-wythe load bearing walls with new structural steel columns and beams. Another portion of the renovation involved reinforcement of an attic floor system in order for the floor to be utilized for office and mechanical room space. Due to the roof slope and the corner of the building next to the new addition; an existing roof truss had to be retrofitted in order to create adequate headroom height in the attic space so that it could be utilized as office space.

Woodford County Court House

Versailles, Kentucky

Client: Woodford County Fiscal Court

Construction Cost: \$3,000,000

Completion Date: 1998

This project's scope of services included design and development of structural plans and specifications, shop drawing review and site inspections of work in progress for a new courthouse.

Sayre School Constitution House

Lexington, Kentucky

Client: Gray Construction

Construction Cost: \$400,000

Completion Date: 2002

This project's scope of services include performing a preliminary inspection of historic structure, assess the structural capacity of the floor system for a change in the usage of the building from a residence to an office, and to provide all necessary drawing documents that are required for this change.

Irvine Renaissance Apartments

Irvine, Kentucky

Client:

Construction Cost: \$1,750,000

Completion Date: 2001

The scope of services for this project involved the historic renovation and constructive re-use of these apartments.

Elizabeth McMurtry House

Lexington, Kentucky

Construction Cost: \$900,000

Completion Date: 2003

The scope of services for this project included the restoration and renovation of an 1886 two and a half story Italianate urban villa. The building was converted from a residence into an office building with two apartments. The renovation consisted of adding a stair tower inside the main structure to access all floors, creating a new entrance opening for the basement, stabilizing and reconstructing the brick veneer, and reconstructing all deteriorated chimneys.

Bourbon County Wright House

Bourbon County, KY

Construction Cost: \$575,000

Completion Date: 2002

This house is an 1880's wood structure purchased by the Department of Transportation to be used as a welcome center as part of the Paris Pike Corridor Restoration. The scope of services consisted of assessing the structural condition of the residence and providing the restructure requirements, and providing the information for this building to be used as a public building.

HENRY CLAY BUILDING (YWCA)

Louisville, KY

Construction cost: \$11,200,000.00

Completion Date: 2008

The nine story building was built in the late 1920's .The structure was use as excrsie facility ,boarding house and ballroom dancing .The scope of services consist of changing the pool area to parking, changing the use to condominium, adding elevator ,stair tower and adding new penthouse floor.

THE NEAL BUILDING

Carlisle, KY

Construction cost: \$850,000.00

Completion Date: 2008

Renovation of historic building for public use, reinforcing the existing floor structure to house public gathering and adding elevator tower inside the building.

December 1, 2015

**RFP #55-2015 Architectural and Engineering Services Kenwick
Community Center Renovation
Affirmative Action Plan**

FITZSIMONS OFFICE of ARCHITECTURE, INC.

112 West Third St. Lexington, KY 40508-1700

fax 859●226●9283

tel 859●243●0838

Fitzsimons Office of Architecture Affirmative Action Plan includes perusing qualified minorities to ensure that our staff is representative of the available work-force in our community.

STW Consulting Engineers has a female partner/principal Cory Sherrod. As the lead mechanical and plumbing engineer she would be responsible for more than fifty percent of the engineering.


Gregory Fitzsimons AIA
C: file

Affirmative Action Plan

All vendors must submit as a part of the proposal package the following items to the Urban County Government:

1. Affirmative Action Plan for his/her firm;
2. Current Work Force Analysis Form;

Failure to submit these items as required may result in disqualification of the submitter from award of the contract. All submissions should be directed to:

Director, Division of Central Purchasing
Lexington-Fayette Urban County Government
200 East Main Street, 3rd Floor
Lexington, Kentucky 40507

All questions regarding this proposal must be directed to the Division of Central Purchasing, (859) 258-3320.

AFFIDAVIT

Comes the Affiant, Gregory Fitzsimons, and after being first duly sworn, states under penalty of perjury as follows:

1. His/her name is Gregory Fitzsimons and he/she is the individual submitting the proposal or is the authorized representative of Fitzsimons Office of Architecture, Inc., the entity submitting the proposal (hereinafter referred to as "Proposer").

2. Proposer will pay all taxes and fees, which are owed to the Lexington-Fayette Urban County Government at the time the proposal is submitted, prior to award of the contract and will maintain a "current" status in regard to those taxes and fees during the life of the contract.

3. Proposer will obtain a Lexington-Fayette Urban County Government business license, if applicable, prior to award of the contract.

4. Proposer has authorized the Division of Central Purchasing to verify the above-mentioned information with the Division of Revenue and to disclose to the Urban County Council that taxes and/or fees are delinquent or that a business license has not been obtained.


5. Proposer has not knowingly violated any provision of the campaign finance laws of the Commonwealth of Kentucky within the past five (5) years and the award of a contract to the Proposer will not violate any provision of the campaign finance laws of the Commonwealth.

6. Proposer has not knowingly violated any provision of Chapter 25 of the Lexington-Fayette Urban County Government Code of Ordinances, known as "Ethics Act."

Continued on next page

7. Proposer acknowledges that "knowingly" for purposes of this Affidavit means, with respect to conduct or to circumstances described by a statute or ordinance defining an offense, that a person is aware or should have been aware that his conduct is of that nature or that the circumstance exists.

Further, Affiant sayeth naught.



STATE OF KENTUCKY

COUNTY OF FAYETTE

The foregoing instrument was subscribed, sworn to and acknowledged before me by GREGORY FITZSIMMONS on this the 22ND day of DECEMBER, 2015.

My Commission expires: 11/8/2016



NOTARY PUBLIC, STATE AT LARGE

476398



EQUAL OPPORTUNITY AGREEMENT

The Law

- Title VII of the Civil Rights Act of 1964 (amended 1972) states that it is unlawful for an employer to discriminate in employment because of race, color, religion, sex, age (40-70 years) or national origin.
- Executive Order No. 11246 on Nondiscrimination under Federal contract prohibits employment discrimination by contractor and sub-contractor doing business with the Federal Government or recipients of Federal funds. This order was later amended by Executive Order No. 11375 to prohibit discrimination on the basis of sex.
- Section 503 of the Rehabilitation Act of 1973 states:

The Contractor will not discriminate against any employee or applicant for employment because of physical or mental handicap.

- Section 2012 of the Vietnam Era Veterans Readjustment Act of 1973 requires Affirmative Action on behalf of disabled veterans and veterans of the Vietnam Era by contractors having Federal contracts.
- Section 206(A) of Executive Order 12086, Consolidation of Contract Compliance Functions for Equal Employment Opportunity, states:

The Secretary of Labor may investigate the employment practices of any Government contractor or sub-contractor to determine whether or not the contractual provisions specified in Section 202 of this order have been violated.

The Lexington-Fayette Urban County Government practices Equal Opportunity in recruiting, hiring and promoting. It is the Government's intent to affirmatively provide employment opportunities for those individuals who have previously not been allowed to enter into the mainstream of society. Because of its importance to the local Government, this policy carries the full endorsement of the Mayor, Commissioners, Directors and all supervisory personnel. In following this commitment to Equal Employment Opportunity and because the Government is the benefactor of the Federal funds, it is both against the Urban County Government policy and illegal for the Government to let contracts to companies which knowingly or unknowingly practice discrimination in their employment practices. Violation of the above mentioned ordinances may cause a contract to be canceled and the contractors may be declared ineligible for future consideration.

Please sign this statement in the appropriate space acknowledging that you have read and understand the provisions contained herein. Return this document as part of your application packet.

Bidders

I/We agree to comply with the Civil Rights Laws listed above that govern employment rights of minorities, women, Vietnam veterans, handicapped and aged persons.

Signature



Name of Business

Fitzsimons Office of Architecture

WORKFORCE ANALYSIS FORM

Name of Organization: Fitzsimons Office of Architecture

Date: 12 / 1 / 15

Categories	Total	White		Latino		Black		Other		Total	
		M	F	M	F	M	F	M	F	M	F
Administrators	1	1								1	
Professionals	1	1								1	
Superintendents											
Supervisors											
Foremen											
Technicians											
Protective Service											
Para-Professionals											
Office/Clerical											
Skilled Craft											
Service/Maintenance											
Total:	2	2								2	

Prepared by: Gregory Fitzsimons, CAO

Name & Title

**DIRECTOR, DIVISION OF CENTRAL PURCHASING
LEXINGTON-FAYETTE URBAN COUNTY GOVERNMENT
200 EAST MAIN STREET
LEXINGTON, KENTUCKY 40507**

**NOTICE OF REQUIREMENT FOR AFFIRMATIVE ACTION TO ENSURE EQUAL
EMPLOYMENT OPPORTUNITIES AND DBE CONTRACT PARTICIPATION**

Notice of requirement for Affirmative Action to ensure Equal Employment Opportunities and Disadvantaged Business Enterprises (DBE) Contract participation. Disadvantaged Business Enterprises (DBE) consists of Minority-Owned Business Enterprises (MBE) and Woman-Owned Business Enterprises (WBE).

The Lexington-Fayette Urban County Government has set a goal that not less than ten percent (10%) of the total value of this Contract be subcontracted to Disadvantaged Business Enterprises, which is made up of MBEs and WBEs. The goal for the utilization of Disadvantaged Business Enterprises as subcontractors is a recommended goal. Contractor(s) who fail to meet such goal will be expected to provide written explanations to the Director of the Division of Purchasing of efforts they have made to accomplish the recommended goal, and the extent to which they are successful in accomplishing the recommended goal will be a consideration in the procurement process. Depending on the funding source, other DBE goals may apply.

For assistance in locating MBE/WBE Subcontractors contact Sherita Miller at 859/258-3320 or by writing the address listed below:

Sherita Miller, Division of Central Purchasing
Lexington-Fayette Urban County Government
200 East Main Street – Room 338
Lexington, Kentucky 40507
smiller@lexingtonky.gov

Firm Submitting Proposal: Fitzsimons Office of Architecture

Complete Address: 112 West Third Street Lexington KY 40508-1700
Street City Zip

Contact Name: Gregory Fitzsimons Title: CAO

Telephone Number: 243-0838 Fax Number: 226-9283

Email address: gftzsimons@foarch.com

Lexington-Fayette Urban County Government
MWDBE PARTICIPATION GOALS

A. GENERAL

- 1) The LFUCG request all potential contractors to make a concerted effort to include Minority-Owned (MBE), Woman-Owned (WBE) and Disadvantaged (DBE) Business Enterprises as subcontractors or suppliers in their bids.
- 2) Toward that end, the LFUCG has established 10% of total procurement costs as a Goal for participation of Minority-Owned, Woman-Owned and Disadvantaged Businesses on this contract.
- 3) **It is therefore a request of each Bidder to include in its bid, the same goal (10%) for MWDBE participation and other requirements as outlined in this section.**

B. PROCEDURES

- 1) The successful bidder will be required to report to the LFUCG, the dollar amounts of all payments submitted to Minority-Owned or Woman-Owned subcontractors and suppliers for work done or materials purchased for this contract. (See Subcontractor Monthly Payment Report)
- 2) Replacement of a Minority-Owned or Woman-Owned subcontractor or supplier listed in the original submittal must be requested in writing and must be accompanied by documentation of Good Faith Efforts to replace the subcontractor / supplier with another MWDBE Firm; this is subject to approval by the LFUCG. (See LFUCG MWDBE Substitution Form)
- 3) For assistance in identifying qualified, certified businesses to solicit for potential contracting opportunities, bidders may contact:
 - a) The Lexington-Fayette Urban County Government, Division of Central Purchasing (859-258-3320)
- 4) The LFUCG will make every effort to notify interested MWDBE subcontractors and suppliers of each Bid Package, including information on the scope of work, the pre-bid meeting time and location, the bid date, and all other pertinent information regarding the project.

C. DEFINITIONS

- 1) A Minority-Owned Business Enterprise (MBE) is defined as a business which is certified as being at least 51% owned and operated by persons of African American, Hispanic, Asian, Pacific Islander, American Indian or Alaskan Native Heritage.

- 2) A Woman-Owned Business Enterprise (WBE) is defined as a business which is certified as being at least 51% owned and operated by one or more Non-Minority Females.
- 3) A Disadvantaged Business (DBE) is defined as a business which is certified as being at least 51% owned and operated by a person(s) that are economically and socially disadvantaged.
- 4) Good Faith Efforts are efforts that, given all relevant circumstances, a bidder or proposer actively and aggressively seeking to meet the goals, can reasonably be expected to make. In evaluating good faith efforts made toward achieving the goals, whether the bidder or proposer has performed the efforts outlined in the Obligations of Bidder for Good Faith Efforts outlined in this document will be considered, along with any other relevant factors.

D. OBLIGATION OF BIDDER FOR GOOD FAITH EFFORTS

- 1) **The bidder shall make a Good Faith Effort to achieve the Participation Goal for MWDBE subcontractors/suppliers. The failure to meet the goal shall not necessarily be cause for disqualification of the bidder; however, bidders not meeting the goal are required to furnish with their bids written documentation of their Good Faith Efforts to do so.**
- 2) Award of Contract shall be conditioned upon satisfaction of the requirements set forth herein.
- 3) The Form of Proposal includes a section entitled “MWDBE Participation Form”. The applicable information must be completed and submitted as outlined below.
- 4) **Failure to submit this information as requested may be cause for rejection of bid.**

E. DOCUMENTATION REQUIRED FOR GOOD FAITH EFFORTS

- 1) Bidders reaching the Goal are required to submit only the MWDBE Participation Form.” The form must be fully completed including names and telephone number of participating MWDBE firm(s); type of work to be performed; estimated value of the contract and value expressed as a percentage of the total Lump Sum Bid Price. The form must be signed and dated, and is to be submitted with the bid.
- 2) Bidders not reaching the Goal must submit the “MWDBE Participation Form”, the “Quote Summary Form” and a written statement documenting their Good Faith Effort to do so. If bid includes no MWDBE participation, bidder shall enter “None” on the subcontractor / supplier

form). In addition, the bidder must submit written proof of their Good Faith Efforts to meet the Participation Goal:

- a. Advertised opportunities to participate in the contract in at least two (2) publications of general circulation media; trade and professional association publications; small and minority business or trade publications; and publications or trades targeting minority, women and disadvantaged businesses not less than fifteen (15) days prior to the deadline for submission of bids to allow MWDBE firms to participate.
- b. Included documentation of advertising in the above publications with the bidders good faith efforts package
- c. Attended LFUCG Central Purchasing Economic Inclusion Outreach event
- d. Attended pre-bid meetings that were scheduled by LFUCG to inform MWDBEs of subcontracting opportunities
- e. Sponsored Economic Inclusion event to provide networking opportunities for prime contractors and MWDBE firms
- f. Requested a list of MWDBE subcontractors or suppliers from LFUCG Economic Engine and showed evidence of contacting the companies on the list(s).
- g. Contacted organizations that work with MWDBE companies for assistance in finding certified MWDBE firms to work on this project. Those contacted and their responses should be a part of the bidder's good faith efforts documentation.
- h. Sent written notices, by certified mail, email or facsimile, to qualified, certified MWDBEs soliciting their participation in the contract not less than seven (7) days prior to the deadline for submission of bids to allow them to participate effectively.
- i. Followed up initial solicitations by contacting MWDBEs to determine their level of interest.
- j. Provided the interested MWDBE firm with adequate and timely information about the plans, specifications, and requirements of the contract.
- k. Selected portions of the work to be performed by MWDBE firms in order to increase the likelihood of meeting the contract goals. This includes, where appropriate, breaking out contract work items into economically feasible units to facilitate MWDBE participation, even

when the prime contractor may otherwise perform these work items with its own workforce.

- l. Negotiated in good faith with interested MWDBE firms not rejecting them as unqualified without sound reasons based on a thorough investigation of their capabilities. Any rejection should be so noted in writing with a description as to why an agreement could not be reached.
- m. Included documentation of quotations received from interested MWDBE firms which were not used due to uncompetitive pricing or were rejected as unacceptable and/or copies of responses from firms indicating that they would not be submitting a bid.
- n. Bidder has to submit sound reasons why the quotations were considered unacceptable. The fact that the bidder has the ability and/or desire to perform the contract work with its own forces will not be considered a sound reason for rejecting a MWDBE quote. Nothing in this provision shall be construed to require the bidder to accept unreasonable quotes in order to satisfy MWDBE goals.
- o. Made an effort to offer assistance to or refer interested MWDBE firms to obtain the necessary equipment, supplies, materials, insurance and/or bonding to satisfy the work requirements of the bid proposal
- p. Made efforts to expand the search for MWBE firms beyond the usual geographic boundaries.
- q. Other--any other evidence that the bidder submits which may show that the bidder has made reasonable good faith efforts to include MWDBE participation.

Failure to submit any of the documentation requested in this section may be cause for rejection of bid. Bidders may include any other documentation deemed relevant to this requirement. Documentation of Good Faith Efforts are to be submitted with the Bid, if the participation Goal is not met.



MINORITY BUSINESS ENTERPRISE PROGRAM

Sherita Miller
Minority Business Enterprise Liaison
Division of Central Purchasing
Lexington-Fayette Urban County Government
200 East Main Street
Lexington, KY 40507
smiller@lexingtonky.gov
859-258-3323

OUR MISSION: The mission of the Minority Business Enterprise Program is to facilitate the full participation of minority and women owned businesses in the procurement process and to promote economic inclusion as a business imperative essential to the long term economic viability of Lexington-Fayette Urban County Government.

To that end the city council adopted and implemented resolution 167-91—Disadvantaged Business Enterprise (DBE) 10% Goal Plan in July of 1991. The resolution states in part (a full copy is available in Central Purchasing):

“A Resolution supporting adoption of the administrative plan for a ten percent (10%) Minimum goal for disadvantaged business enterprise participation in Lexington-Fayette Urban County Government construction and professional services contracts; Providing that as part of their bids on LFUCG construction contracts, general Contractors shall make a good faith effort to award at least ten percent (10%) of All subcontracts to disadvantaged business enterprises; providing that divisions of LFUCG shall make a good faith effort to award at least ten percent of their Professional services and other contracts to disadvantaged business enterprises...”

A Disadvantaged Business Enterprise is defined as a business that has been certified as being at least 51% owned, operated and managed by a U.S. Citizen of the following groups:

- African-American
- Hispanic-American
- Asian/Pacific Islander
- Native American/Native Alaskan
- Non-Minority Female
- Economically and Socially Disadvantaged

We have compiled the list below to help you locate certified MBE, WBE and DBE certified businesses. Below is a listing of contacts for LFUCG Certified MWDBEs in Economic Engine (<https://lfucg.economicengine.com>)

Business	Contact	Email Address	Phone
LFUCG	Sherita Miller	smiller@lexingtonky.gov	859-258-3323
Commerce Lexington – Minority Business Development	Tyrone Tyra	tyra@commercelexington.com	859-226-1625
Tri-State Minority Supplier Diversity Council	Sonya Brown	sbrown@tsmsdc.com	502-625-0137
Small Business Development Council	Dee Dee Harbut UK SBDC	dharbut@uky.edu	
	Shiree Mack	smack@uky.edu	
Community Ventures Corporation	James Coles	jcoles@cycky.org	859-231-0054
KY Department of Transportation	Melvin Bynes	Melvin.bynes@ky.gov	502-564-3601
	Shella Eagle	Shella.Eagle@ky.gov	502-564-3601
Ohio River Valley Women’s Business Council (WBENC)	Rea Waldon	rwaldon@gcul.org	513-487-6534
Kentucky MWBE Certification Program	Yvette Smith, Kentucky Finance Cabinet	Yvette.Smith@ky.gov	502-564-8099
National Women Business Owner’s Council (NWBOC)	Janet Harris-Lange	janet@nwbo.org	800-675-5066
Small Business Administration	Robert Coffey	robertcoffey@sba.gov	502-582-5971
LaVoz de Kentucky	Andres Cruz	lavozydeky@yahoo.com	859-621-2106
The Key News Journal	Patrice Muhammad	paatricem@keynewsjournal.com	859-373-9428



LFUCG MWDBE PARTICIPATION FORM

Bid/RFP/Quote Reference # 56-2015 Castlewood

The MWDBE subcontractors listed have agreed to participate on this Bid/RFP/Quote. If any substitution is made or the total value of the work is changed prior to or after the job is in progress, it is understood that those substitutions must be submitted to Central Purchasing for approval immediately.

MWDBE Company, Name, Address, Phone, Email	Work to be Performed	Total Dollar Value of the Work	% Value of Total Contract
1.			
2.			
3.			
4.			

The undersigned company representative submits the above list of MWDBE firms to be used in accomplishing the work contained in this Bid/RFP/Quote. Any misrepresentation may result in the termination of the contract and/or be subject to applicable Federal and State laws concerning false statements and false claims.

Fitzsimons Office of Architecture

Company

12/1/15

Date

Company Representative

CAO

Title



LFUCG MWDBE SUBSTITUTION FORM

Bid/RFP/Quote Reference # 56-2015 Castlewood

The substituted MWDBE subcontractors listed below have agreed to participate on this Bid/RFP/Quote. These substitutions were made prior to or after the job was in progress. These substitutions were made for reasons stated below and are now being submitted to Central Purchasing for approval. By the authorized signature of a representative of our company, we understand that this information will be entered into our file for this project.

SUBSTITUTED MWDBE Company Name, Address, Phone, Email	MWDBE Formally Contracted/ Name, Address, Phone, Email	Work to Be Performed	Reason for the Substitution	Total Dollar Value of the Work	% Value of Total Contract
1.					
2.					
3.					
4.					

The undersigned acknowledges that any misrepresentation may result in termination of the contract and/or be subject to applicable Federal and State laws concerning false statements and false claims.

Fitzsimons Office of Architecture
Company

12/1/15
Date


Company Representative

CAO
Title



MWDBE QUOTE SUMMARY FORM

Bid/RFP/Quote Reference # 56-2015 Castlewood

The undersigned acknowledges that the minority subcontractors listed on this form did submit a quote to participate on this project.

Company Name Fitzsimons Office of Architecture	Contact Person Gregory Fitzsimons
Address/Phone/Email 112 West Third St. Lexington, KY 40508	Bid Package / Bid Date 56-2015 Castlewood 12/22/15

MWDBE Company Address	Contact Person	Contact Information (work phone, Email, cell)	Date Contacted	Services to be performed	Method of Communication (email, phone meeting, ad, event etc)	Total dollars \$\$ Do Not Leave Blank (Attach Documentation)	MBE * AA HA AS NA Female

(MBE designation / AA=African American / HA= Hispanic American/AS = Asian American/Pacific Islander/ NA= Native American)

The undersigned acknowledges that all information is accurate. Any misrepresentation may result in termination of the contract and/or be subject to applicable Federal and State laws concerning false statements and claims.

Fitzsimons Office of Architecture
Company

12/1/15
Date


Company Representative

CAO
Title



LFUCG SUBCONTRACTOR MONTHLY PAYMENT REPORT

The LFUCG has a 10% goal plan adopted by city council to increase the participation of minority and women owned businesses in the procurement process. In order to measure that goal LFUCG will track spending with MWDBE vendors on a monthly basis. By the signature below of an authorized company representative, you certify that the information is correct, and that each of the representations set forth below is true. Any misrepresentation may result in termination of the contract and/or prosecution under applicable Federal and State laws concerning false statements and false claims. Please submit this form monthly to the Division of Central Purchasing/ 200 East Main Street / Room 338 / Lexington, KY 40507.

Bid/RFP/Quote # 56-2015 Castlewood
Total Contract Amount Awarded to Prime Contractor for this Project \$18,000.00

Project Name/ Contract #	Work Period/ From: _____ To: _____
Company Name:	Address:
Federal Tax ID:	Contact Person:

Subcontractor Vendor ID (name, address, phone, email)	Description of Work	Total Subcontract Amount	% of Total Contract Awarded to Prime for this Project	Total Amount Paid for this Period	Purchase Order number for subcontractor work (please attach PO)	Scheduled Project Start Date	Scheduled Project End Date

By the signature below of an authorized company representative, you certify that the information is correct, and that each of the representations set forth below is true. Any misrepresentations may result in the termination of the contract and/or prosecution under applicable Federal and State laws concerning false statements and false claims.

Fitzsimons Office of Architecture
Company
12/1/15
Date



Company Representative
CAO
Title

LFUCG STATEMENT OF GOOD FAITH EFFORTS

Bid/RFP/Quote # 56-2015 Castlewood

By the signature below of an authorized company representative, we certify that we have utilized the following Good Faith Efforts to obtain the maximum participation by MWDBE business enterprises on the project and can supply the appropriate documentation.

_____ Advertised opportunities to participate in the contract in at least two (2) publications of general circulation media; trade and professional association publications; small and minority business or trade publications; and publications or trades targeting minority, women and disadvantaged businesses not less than fifteen (15) days prior to the deadline for submission of bids to allow MWDBE firms to participate.

_____ Included documentation of advertising in the above publications with the bidders good faith efforts package

_____ Attended LFUCG Central Purchasing Economic Inclusion Outreach event

_____ Attended pre-bid meetings that were scheduled by LFUCG to inform MWDBEs of subcontracting opportunities

_____ Sponsored Economic Inclusion event to provide networking opportunities for prime contractors and MWDBE firms

_____ Requested a list of MWDBE subcontractors or suppliers from LFUCG Economic Engine and showed evidence of contacting the companies on the list(s).

_____ Contacted organizations that work with MWDBE companies for assistance in finding certified MWDBE firms to work on this project. Those contacted and their responses should be a part of the bidder's good faith efforts documentation.

_____ Sent written notices, by certified mail, email or facsimile, to qualified, certified MWDBEs soliciting their participation in the contract not less than seven (7) days prior to the deadline for submission of bids to allow them to participate effectively.

_____ Followed up initial solicitations by contacting MWDBEs to determine their level of interest.

- _____ Provided the interested MWDBE firm with adequate and timely information about the plans, specifications, and requirements of the contract.
- _____ Selected portions of the work to be performed by MWDBE firms in order to increase the likelihood of meeting the contract goals. This includes, where appropriate, breaking out contract work items into economically feasible units to facilitate MWDBE participation, even when the prime contractor may otherwise perform these work items with its own workforce
- _____ Negotiated in good faith with interested MWDBE firms not rejecting them as unqualified without sound reasons based on a thorough investigation of their capabilities. Any rejection should be so noted in writing with a description as to why an agreement could not be reached.
- _____ Included documentation of quotations received from interested MWDBE firms which were not used due to uncompetitive pricing or were rejected as unacceptable and/or copies of responses from firms indicating that they would not be submitting a bid.
- _____ Bidder has to submit sound reasons why the quotations were considered unacceptable. The fact that the bidder has the ability and/or desire to perform the contract work with its own forces will not be considered a sound reason for rejecting a MWDBE quote. Nothing in this provision shall be construed to require the bidder to accept unreasonable quotes in order to satisfy MWDBE goals.
- _____ Made an effort to offer assistance to or refer interested MWDBE firms to obtain the necessary equipment, supplies, materials, insurance and/or bonding to satisfy the work requirements of the bid proposal
- _____ Made efforts to expand the search for MWBE firms beyond the usual geographic boundaries.
- _____ Other - any other evidence that the bidder submits which may show that the bidder has made reasonable good faith efforts to include MWDBE participation.

Failure to submit any of the documentation requested in this section may be cause for rejection of bid. Bidders may include any other documentation deemed relevant to this requirement. Documentation of Good Faith Efforts are to be submitted with the Bid, if the participation Goal is not met.

The undersigned acknowledges that all information is accurate. Any misrepresentations may result in termination of the contract and/or be subject to applicable Federal and State laws concerning false statements and claims.

Fitzsimons Office of Architecture



Company

Company Representative

12/1/15

CAO

Date

Title

GENERAL PROVISIONS

1. Each Respondent shall comply with all Federal, State & Local regulations concerning this type of service or good.

The Respondent agrees to comply with all statutes, rules, and regulations governing safe and healthful working conditions, including the Occupational Health and Safety Act of 1970, *29 U.S.C. 650 et. seq.*, as amended, and KRS Chapter 338. The Respondent also agrees to notify the LFUCG in writing immediately upon detection of any unsafe and/or unhealthful working conditions at the job site. The Respondent agrees to indemnify, defend and hold the LFUCG harmless from all penalties, fines or other expenses arising out of the alleged violation of said laws.

2. Failure to submit ALL forms and information required in this RFP may be grounds for disqualification.
3. Addenda: All addenda, if any, shall be considered in making the proposal, and such addenda shall be made a part of this RFP. Before submitting a proposal, it is incumbent upon each proposer to be informed as to whether any addenda have been issued, and the failure to cover in the bid any such addenda may result in disqualification of that proposal.
4. Proposal Reservations: LFUCG reserves the right to reject any or all proposals, to award in whole or part, and to waive minor immaterial defects in proposals. LFUCG may consider any alternative proposal that meets its basic needs.
5. Liability: LFUCG is not responsible for any cost incurred by a Respondent in the preparation of proposals.
6. Changes/Alterations: Respondent may change or withdraw a proposal at any time prior to the opening; however, no oral modifications will be allowed. Only letters, or other formal written requests for modifications or corrections of a previously submitted proposal which is addressed in the same manner as the proposal, and received by LFUCG prior to the scheduled closing time for receipt of proposals, will be accepted. The proposal, when opened, will then be corrected in accordance with such written request(s), provided that the written request is contained in a sealed envelope which is plainly marked "modifications of proposal".
7. Clarification of Submittal: LFUCG reserves the right to obtain clarification of any point in a bid or to obtain additional information from a Respondent.
8. Bribery Clause: By his/her signature on the bid, Respondent certifies that no employee of his/hers, any affiliate or Subcontractor, has bribed or

attempted to bribe an officer or employee of the LFUCG.

9. Additional Information: While not necessary, the Respondent may include any product brochures, software documentation, sample reports, or other documentation that may assist LFUCG in better understanding and evaluating the Respondent's response. Additional documentation shall not serve as a substitute for other documentation which is required by this RFP to be submitted with the proposal,
10. Ambiguity, Conflict or other Errors in RFP: If a Respondent discovers any ambiguity, conflict, discrepancy, omission or other error in the RFP, it shall immediately notify LFUCG of such error in writing and request modification or clarification of the document if allowable by the LFUCG.
11. Agreement to Bid Terms: In submitting this proposal, the Respondent agrees that it has carefully examined the specifications and all provisions relating to the work to be done attached hereto and made part of this proposal. By acceptance of a Contract under this RFP, proposer states that it understands the meaning, intent and requirements of the RFP and agrees to the same. The successful Respondent shall warrant that it is familiar with and understands all provisions herein and shall warrant that it can comply with them. No additional compensation to Respondent shall be authorized for services or expenses reasonably covered under these provisions that the proposer omits from its Proposal.
12. Cancellation: If the services to be performed hereunder by the Respondent are not performed in an acceptable manner to the LFUCG, the LFUCG may cancel this contract for cause by providing written notice to the proposer, giving at least thirty (30) days notice of the proposed cancellation and the reasons for same. During that time period, the proposer may seek to bring the performance of services hereunder to a level that is acceptable to the LFUCG, and the LFUCG may rescind the cancellation if such action is in its best interest.

A. Termination for Cause

- (1) LFUCG may terminate a contract because of the contractor's failure to perform its contractual duties
- (2) If a contractor is determined to be in default, LFUCG shall notify the contractor of the determination in writing, and may include a specified date by which the contractor shall cure the identified deficiencies. LFUCG may proceed with termination if the contractor fails to cure the deficiencies within the specified time.


- (3) A default in performance by a contractor for which a contract may be terminated shall include, but shall not necessarily be limited to:
- (a) Failure to perform the contract according to its terms, conditions and specifications;
 - (b) Failure to make delivery within the time specified or according to a delivery schedule fixed by the contract;
 - (c) Late payment or nonpayment of bills for labor, materials, supplies, or equipment furnished in connection with a contract for construction services as evidenced by mechanics' liens filed pursuant to the provisions of KRS Chapter 376, or letters of indebtedness received from creditors by the purchasing agency;
 - (d) Failure to diligently advance the work under a contract for construction services;
 - (e) The filing of a bankruptcy petition by or against the contractor; or
 - (f) Actions that endanger the health, safety or welfare of the LFUCG or its citizens.

B. At Will Termination

Notwithstanding the above provisions, the LFUCG may terminate this contract at will in accordance with the law upon providing thirty (30) days written notice of that intent, Payment for services or goods received prior to termination shall be made by the LFUCG provided these goods or services were provided in a manner acceptable to the LFUCG. Payment for those goods and services shall not be unreasonably withheld.

13. **Assignment of Contract:** The contractor shall not assign or subcontract any portion of the Contract without the express written consent of LFUCG. Any purported assignment or subcontract in violation hereof shall be void. It is expressly acknowledged that LFUCG shall never be required or obligated to consent to any request for assignment or subcontract; and further that such refusal to consent can be for any or no reason, fully within the sole discretion of LFUCG.
14. **No Waiver:** No failure or delay by LFUCG in exercising any right, remedy, power or privilege hereunder, nor any single or partial exercise thereof, nor the exercise of any other right, remedy, power or privilege shall operate as a waiver hereof or thereof. No failure or delay by LFUCG in exercising any right, remedy, power or privilege under or in respect of this Contract shall affect the rights, remedies, powers or privileges of LFUCG hereunder or shall operate as a waiver thereof.

15. Authority to do Business: The Respondent must be a duly organized and authorized to do business under the laws of Kentucky. Respondent must be in good standing and have full legal capacity to provide the services specified under this Contract. The Respondent must have all necessary right and lawful authority to enter into this Contract for the full term hereof and that proper corporate or other action has been duly taken authorizing the Respondent to enter into this Contract. The Respondent will provide LFUCG with a copy of a corporate resolution authorizing this action and a letter from an attorney confirming that the proposer is authorized to do business in the State of Kentucky if requested. All proposals must be signed by a duly authorized officer, agent or employee of the Respondent.
16. Governing Law: This Contract shall be governed by and construed in accordance with the laws of the Commonwealth of Kentucky. In the event of any proceedings regarding this Contract, the Parties agree that the venue shall be the Fayette County Circuit Court or the U.S. District Court for the Eastern District of Kentucky, Lexington Division. All parties expressly consent to personal jurisdiction and venue in such Court for the limited and sole purpose of proceedings relating to this Contract or any rights or obligations arising thereunder. Service of process may be accomplished by following the procedures prescribed by law.
17. Ability to Meet Obligations: Respondent affirmatively states that there are no actions, suits or proceedings of any kind pending against Respondent or, to the knowledge of the Respondent, threatened against the Respondent before or by any court, governmental body or agency or other tribunal or authority which would, if adversely determined, have a materially adverse effect on the authority or ability of Respondent to perform its obligations under this Contract, or which question the legality, validity or enforceability hereof or thereof.
18. Contractor understands and agrees that its employees, agents, or subcontractors are not employees of LFUCG for any purpose whatsoever. Contractor is an independent contractor at all times during the performance of the services specified.
19. If any term or provision of this Contract shall be found to be illegal or unenforceable, the remainder of the contract shall remain in full force and such term or provision shall be deemed stricken.

Signature 

12/1/15

Date



Lexington-Fayette Urban County Government
DEPARTMENT OF FINANCE & ADMINISTRATION

Jim Gray
Mayor

William O'Mara
Commissioner

ADDENDUM #1

RFP Number: **#56-2015**

Date: December 11, 2015

Subject: Architectural and Engineering Services for Castlewood
Community Center Renovation

Address inquiries to:
Sondra Stone
(859) 258-3320

TO ALL PROSPECTIVE SUBMITTERS:

Please be advised of the following clarifications to the above referenced RFP:

The Professional Liability requirement has been changed to \$1 million per occurrence, \$2 million aggregate.

Todd Slatin, Director
Division of Central Purchasing

All other terms and conditions of the Bid and specifications are unchanged.
This letter should be signed, attached to and become a part of your Bid.

COMPANY NAME: Fitzsimons Office of Architecture

ADDRESS: 112 West Third St., Lexington, KY 40508

SIGNATURE OF BIDDER:



FITZSIMONS OFFICE of ARCHITECTURE, INC.

112 West Third St. Lexington, KY 40508-1700

fax 859•226•9283

tel 859•243•0838

Acorn Ave

Castlewood Dr

Avon Ave

Burnett Ave

Bryan Ave

Maple Ave
